


**RIC-30-11.56  
Project 486(02)**

**Phase 1  
(March 1, 2003 to September 16, 2003)**

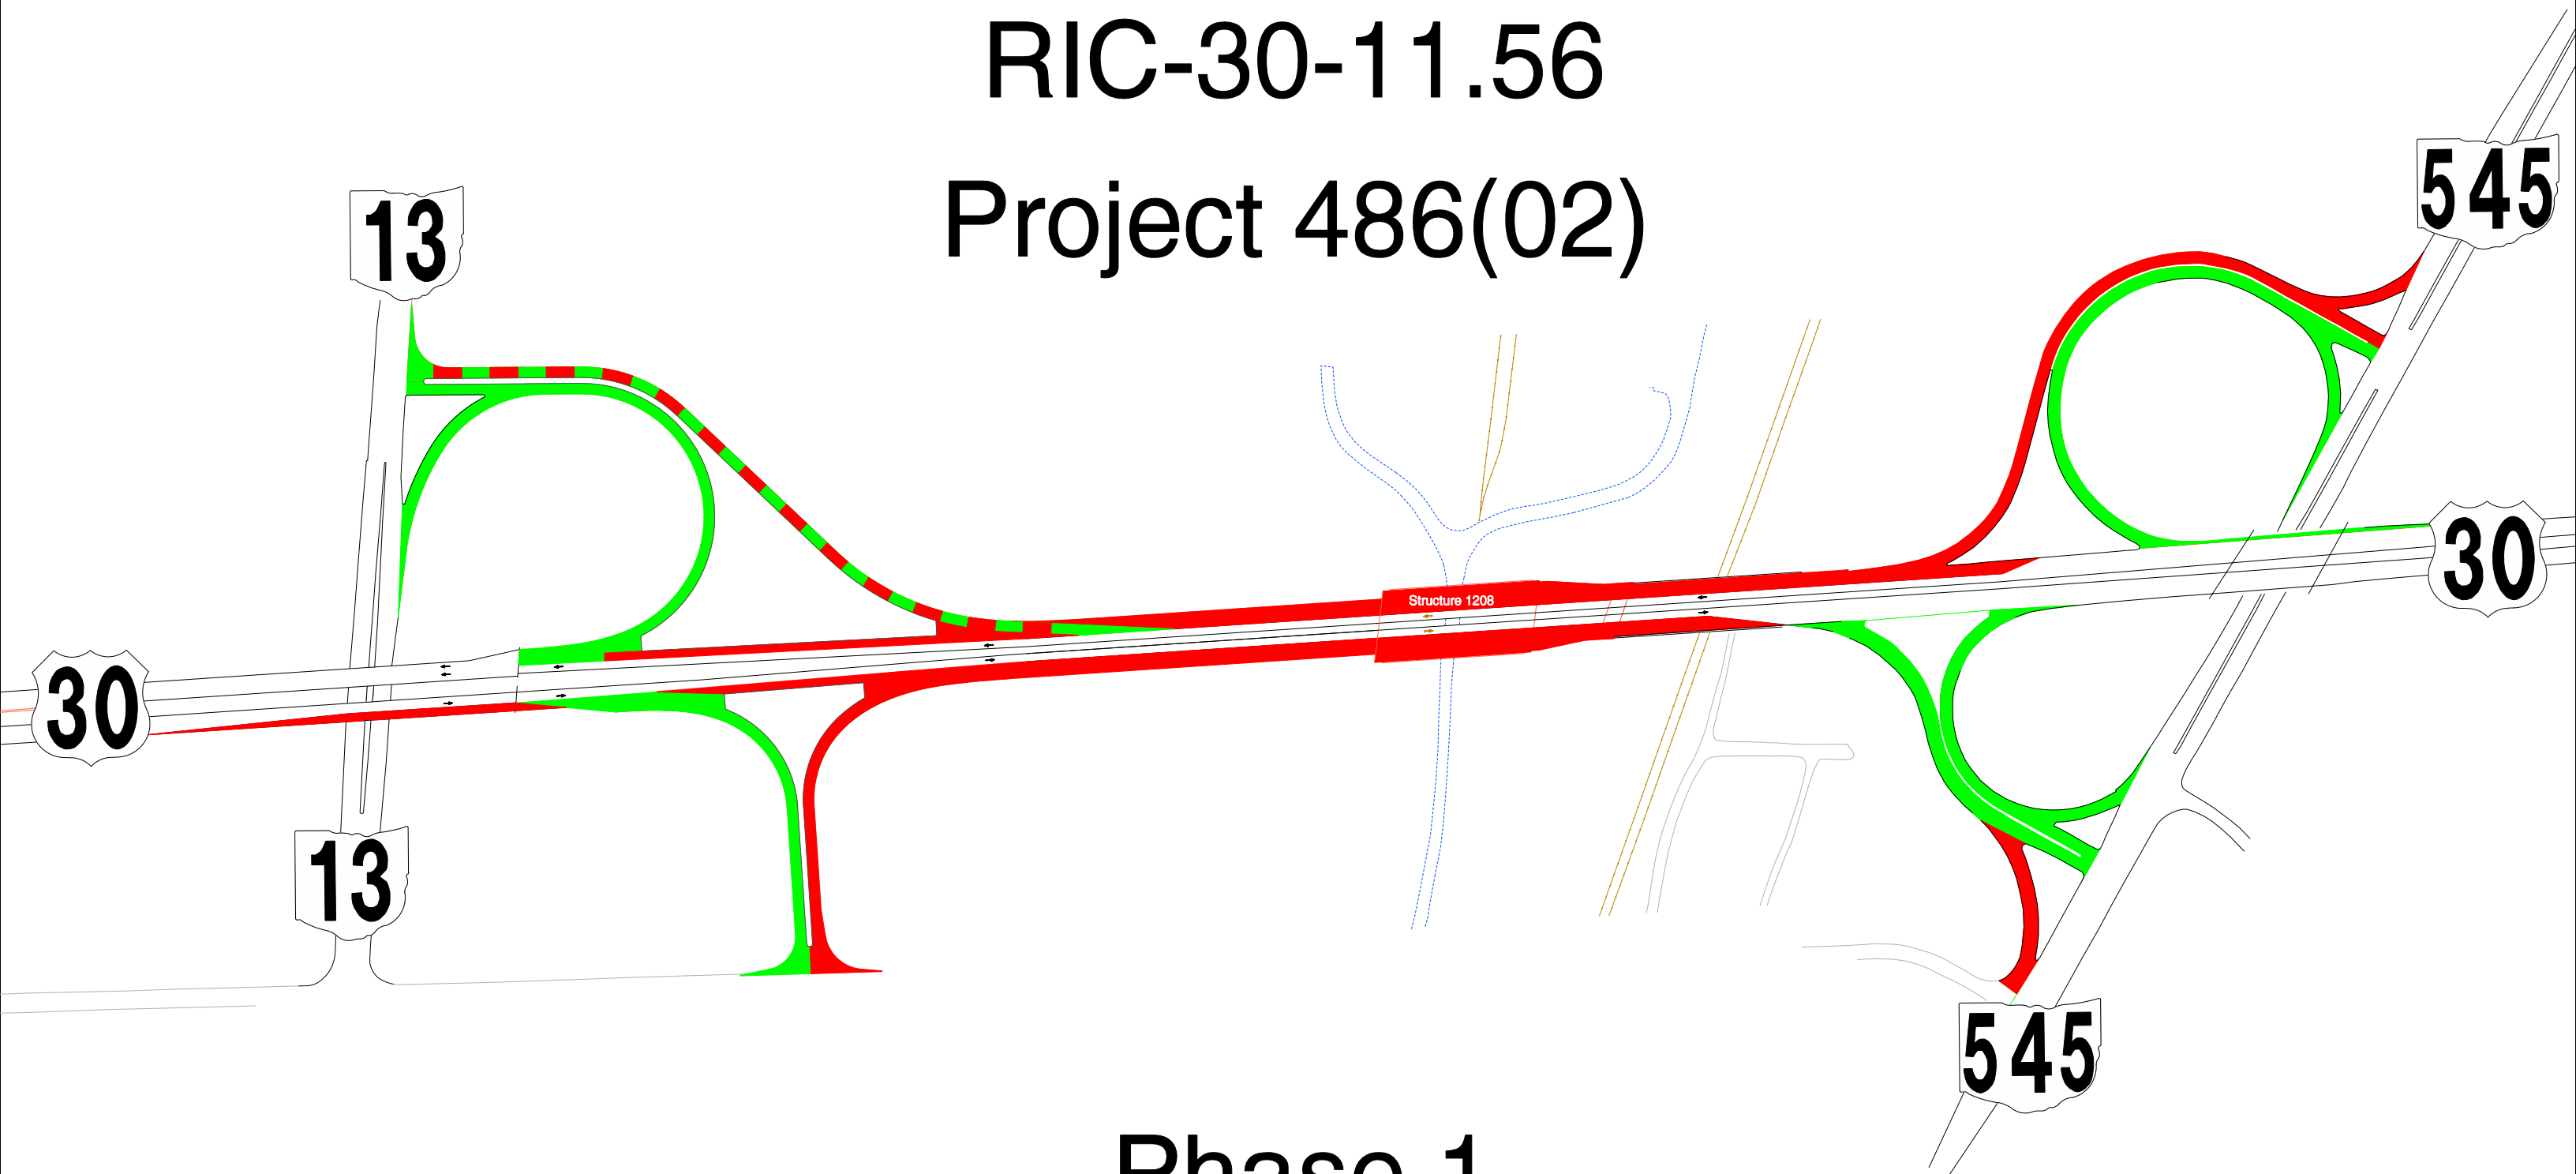


- ✓ Build outside phase of Structure 1208
- ✓ One Lane of Traffic each direction on inside lanes.
- ✓ Close eastbound entrance ramp SR-13
- ✓ Close westbound exit ramp to SR-13 for maximum of 2 months.
- ✓ Close westbound entrance ramp from SR-545
- ✓ Temporary signal at SR-545/Longview

# RIC-30-11.56 Project 486(02)



## Phase 1


March 1, 2003 to June 30, 2003

-  Closed
-  Open
-  Closed for 2 months

RIC-30-11.56  
Project 486(02)

Phase 1

March 1, 2003 to June 30, 2003

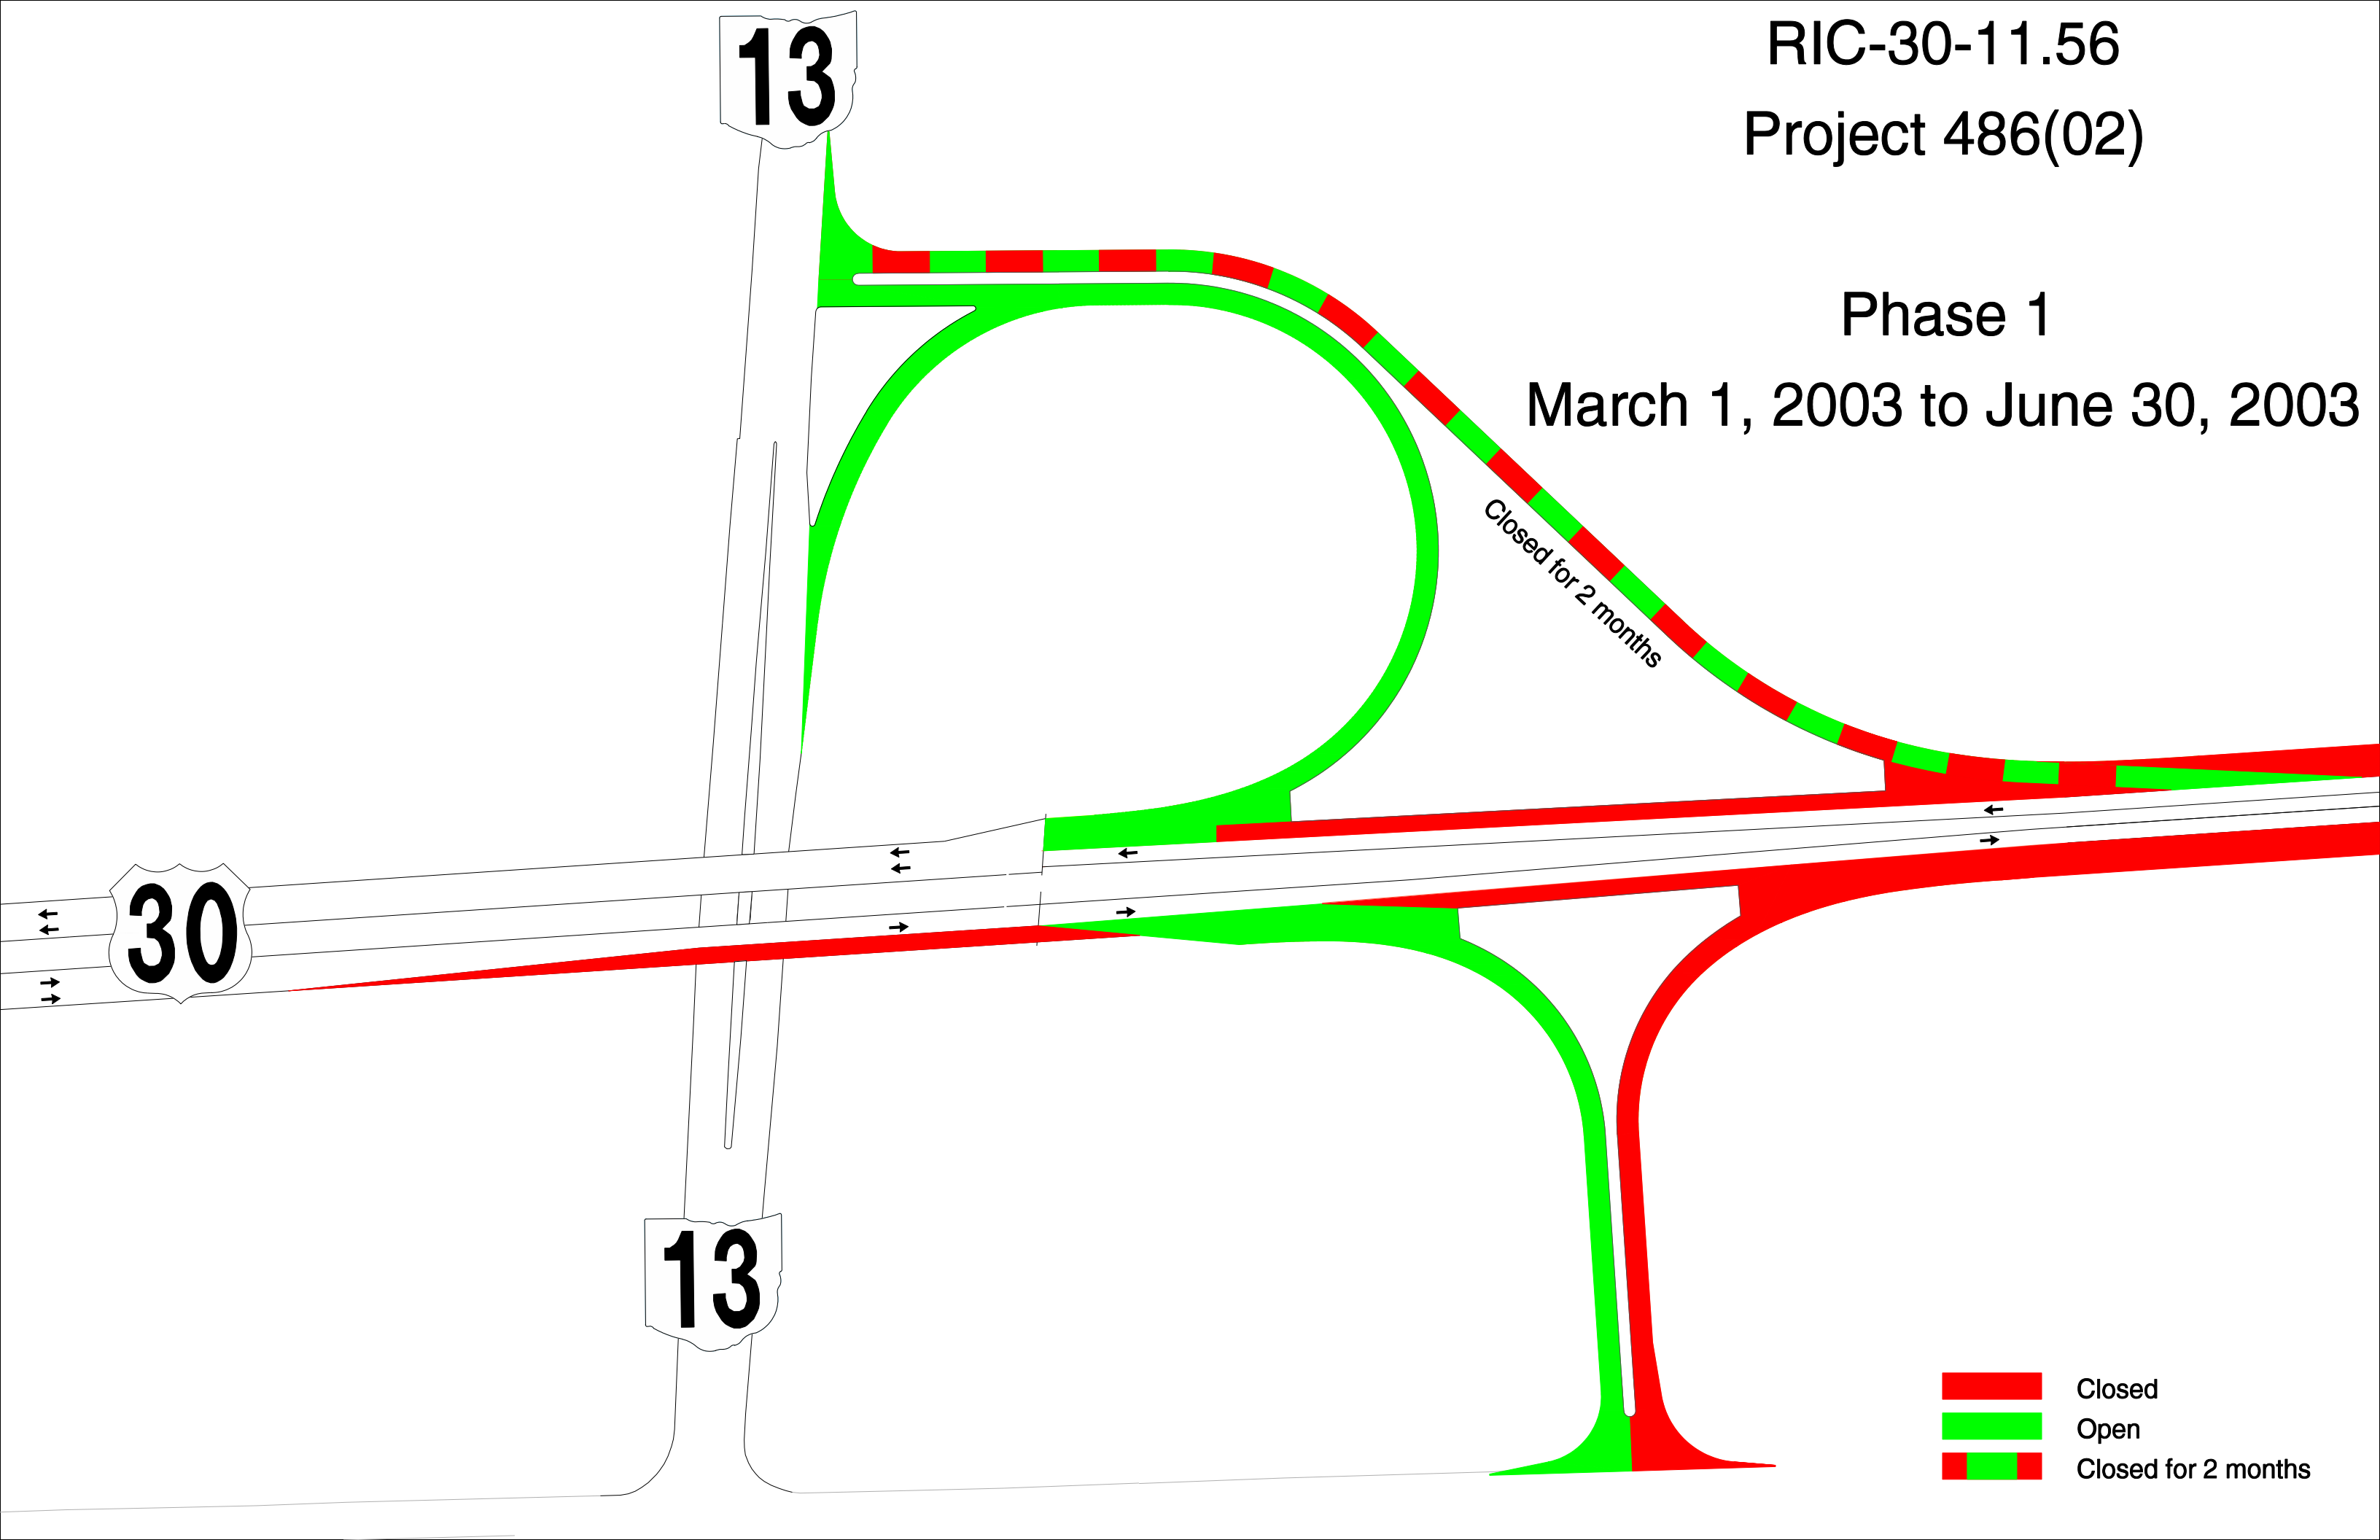




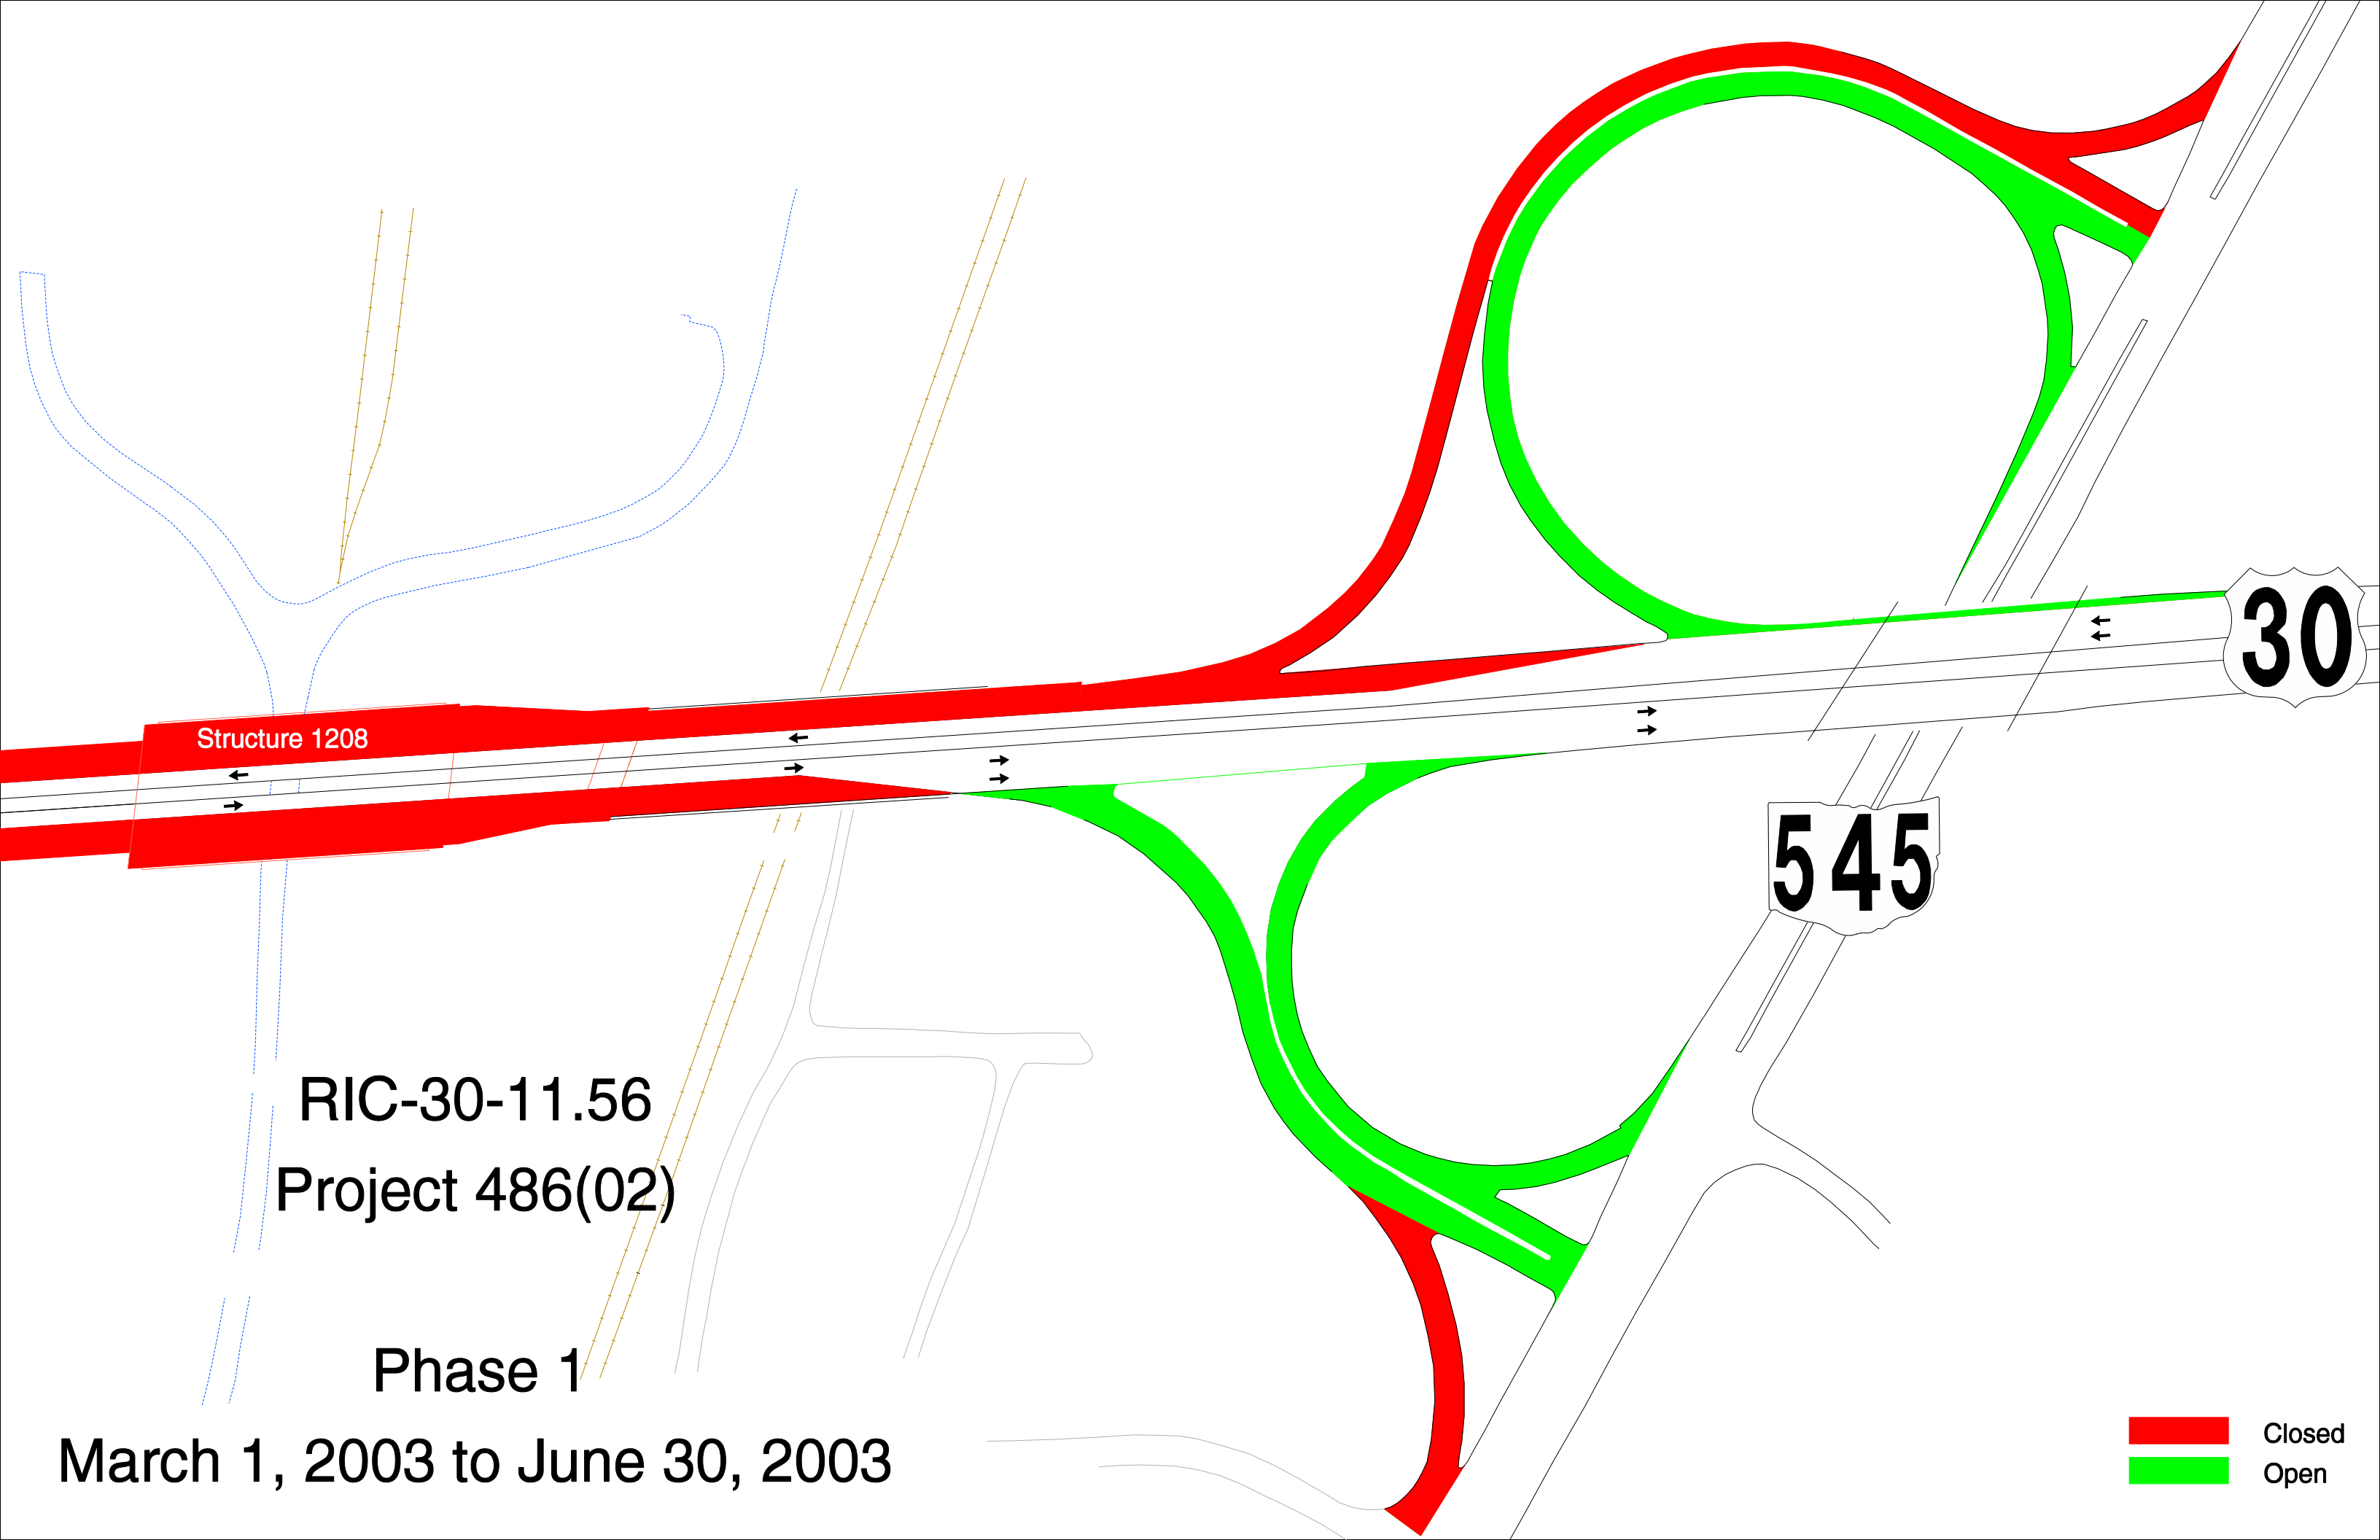
13

30

13

Closed for 2 months

-  Closed
-  Open
-  Closed for 2 months



Structure 1208

RIC-30-11.56  
Project 486(02)

Phase 1

March 1, 2003 to June 30, 2003

30

545


Closed  
Open

**RIC-30-11.56**  
**Project 486(02)**

**Phase 2**  
**(September 16, 2003 to November 20, 2003)**

- ✓ Build inside phase of Structure 1208
- ✓ One Lane Traffic each direction on outside lanes.
- ✓ Keep Eastbound entrance ramp from SR-13 closed.
- ✓ Keep Westbound entrance ramp from SR-545 closed.
- ✓ Maintain temporary signal at SR-545/Longview

# RIC-30-11.56 Project 486(02)

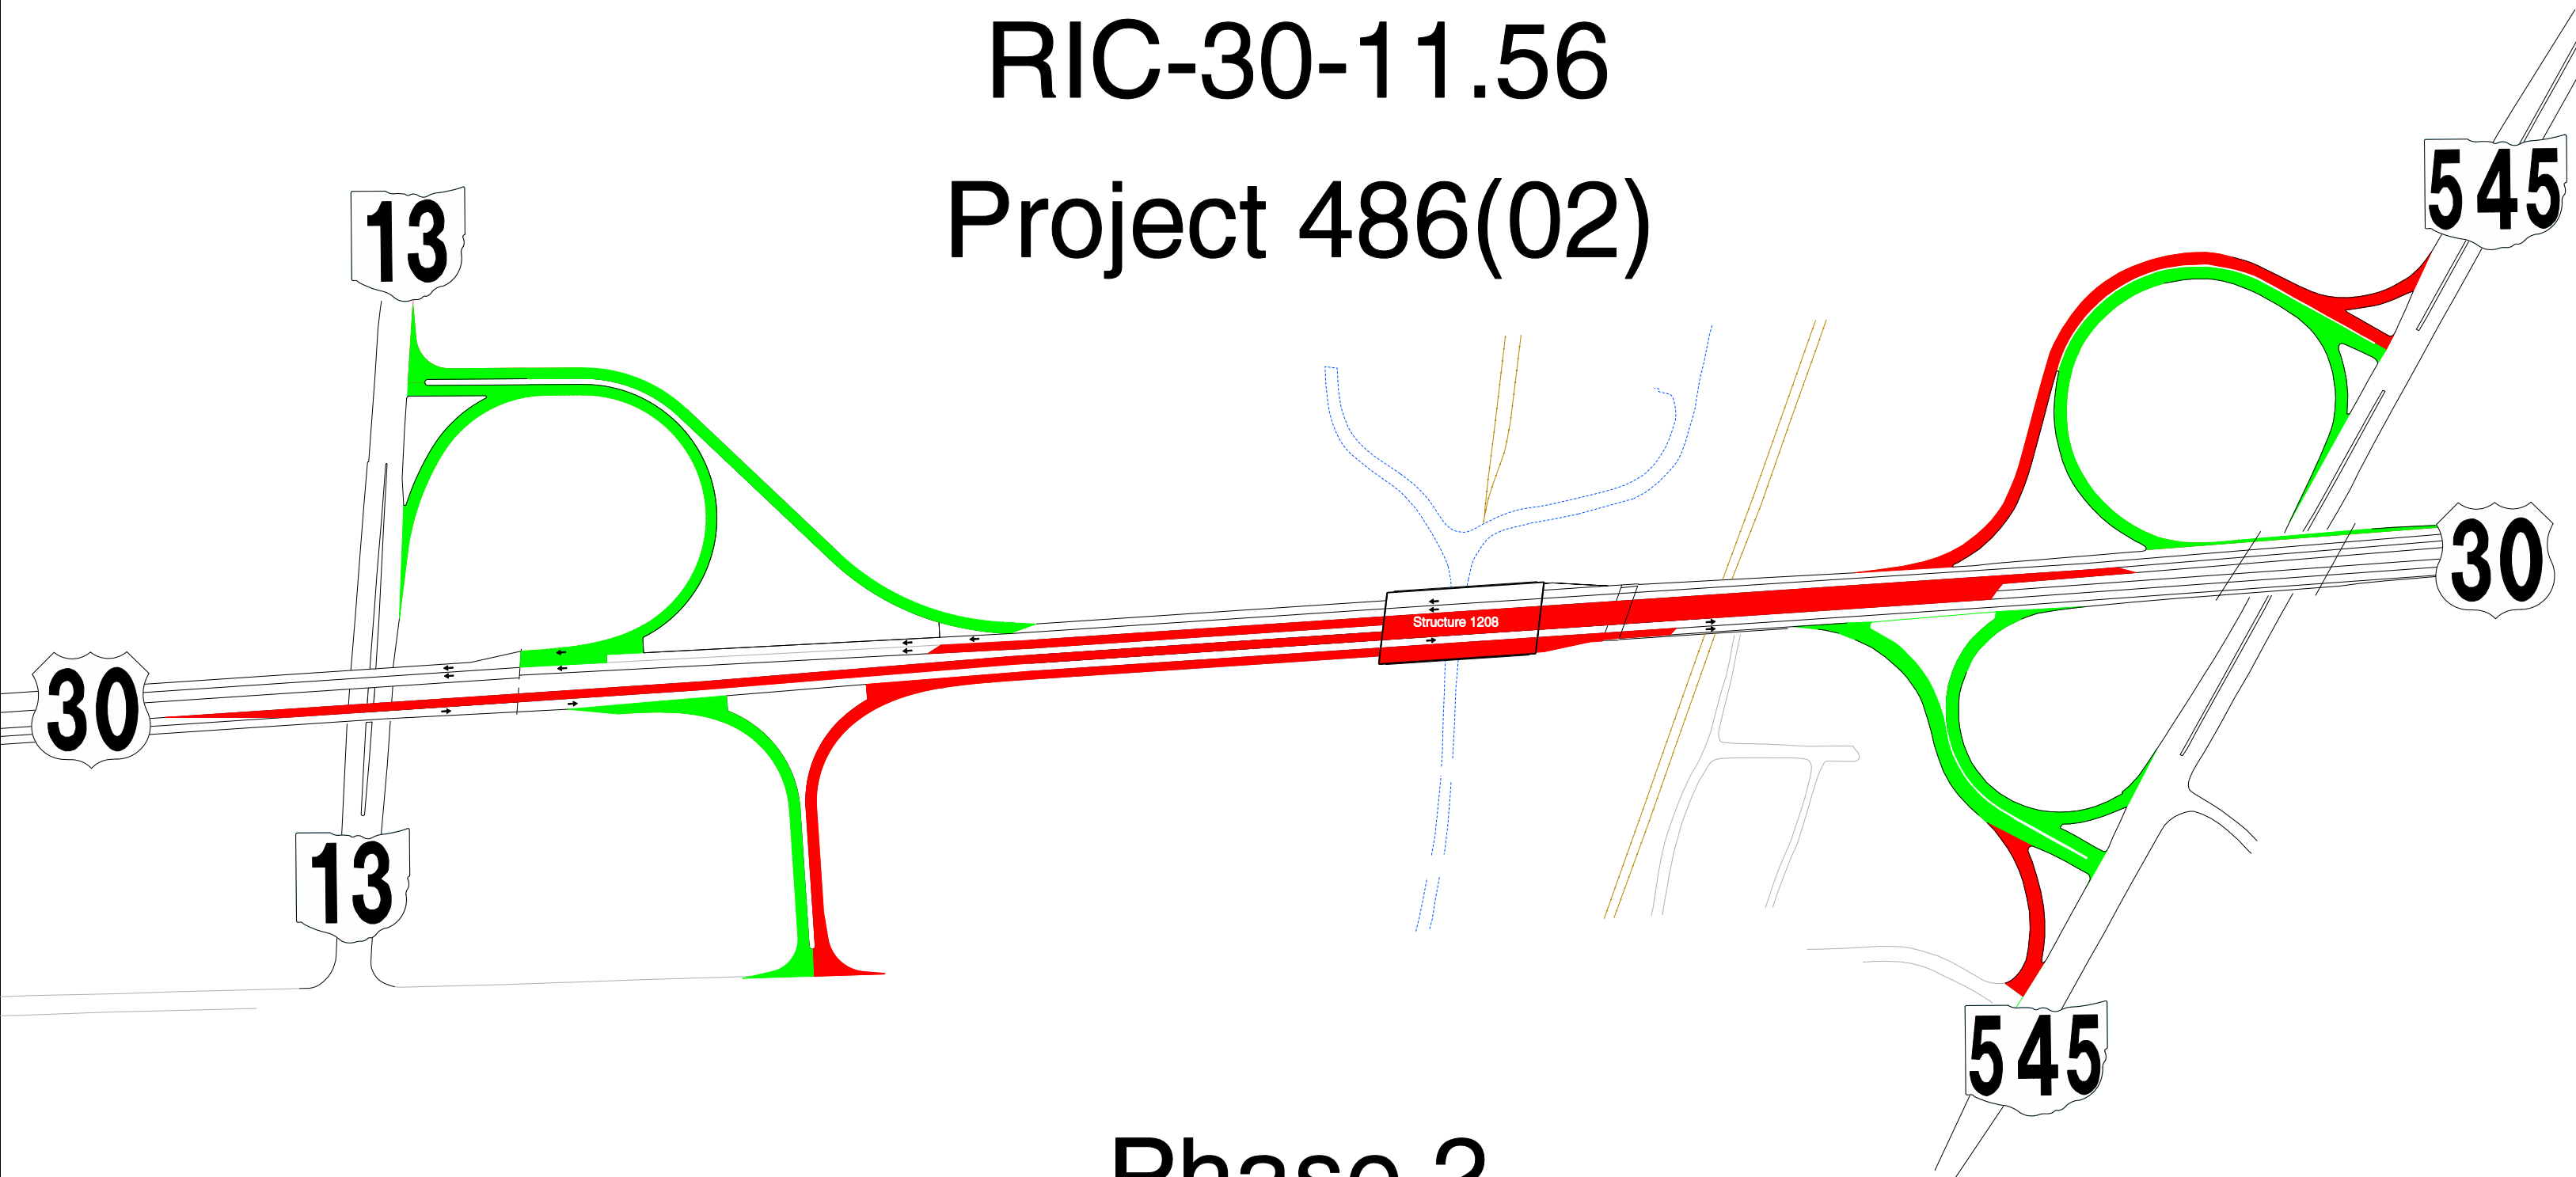


## Phase 2

July 1, 2003 to October 31, 2003

 Closed  
 Open


 Closed  
 Open

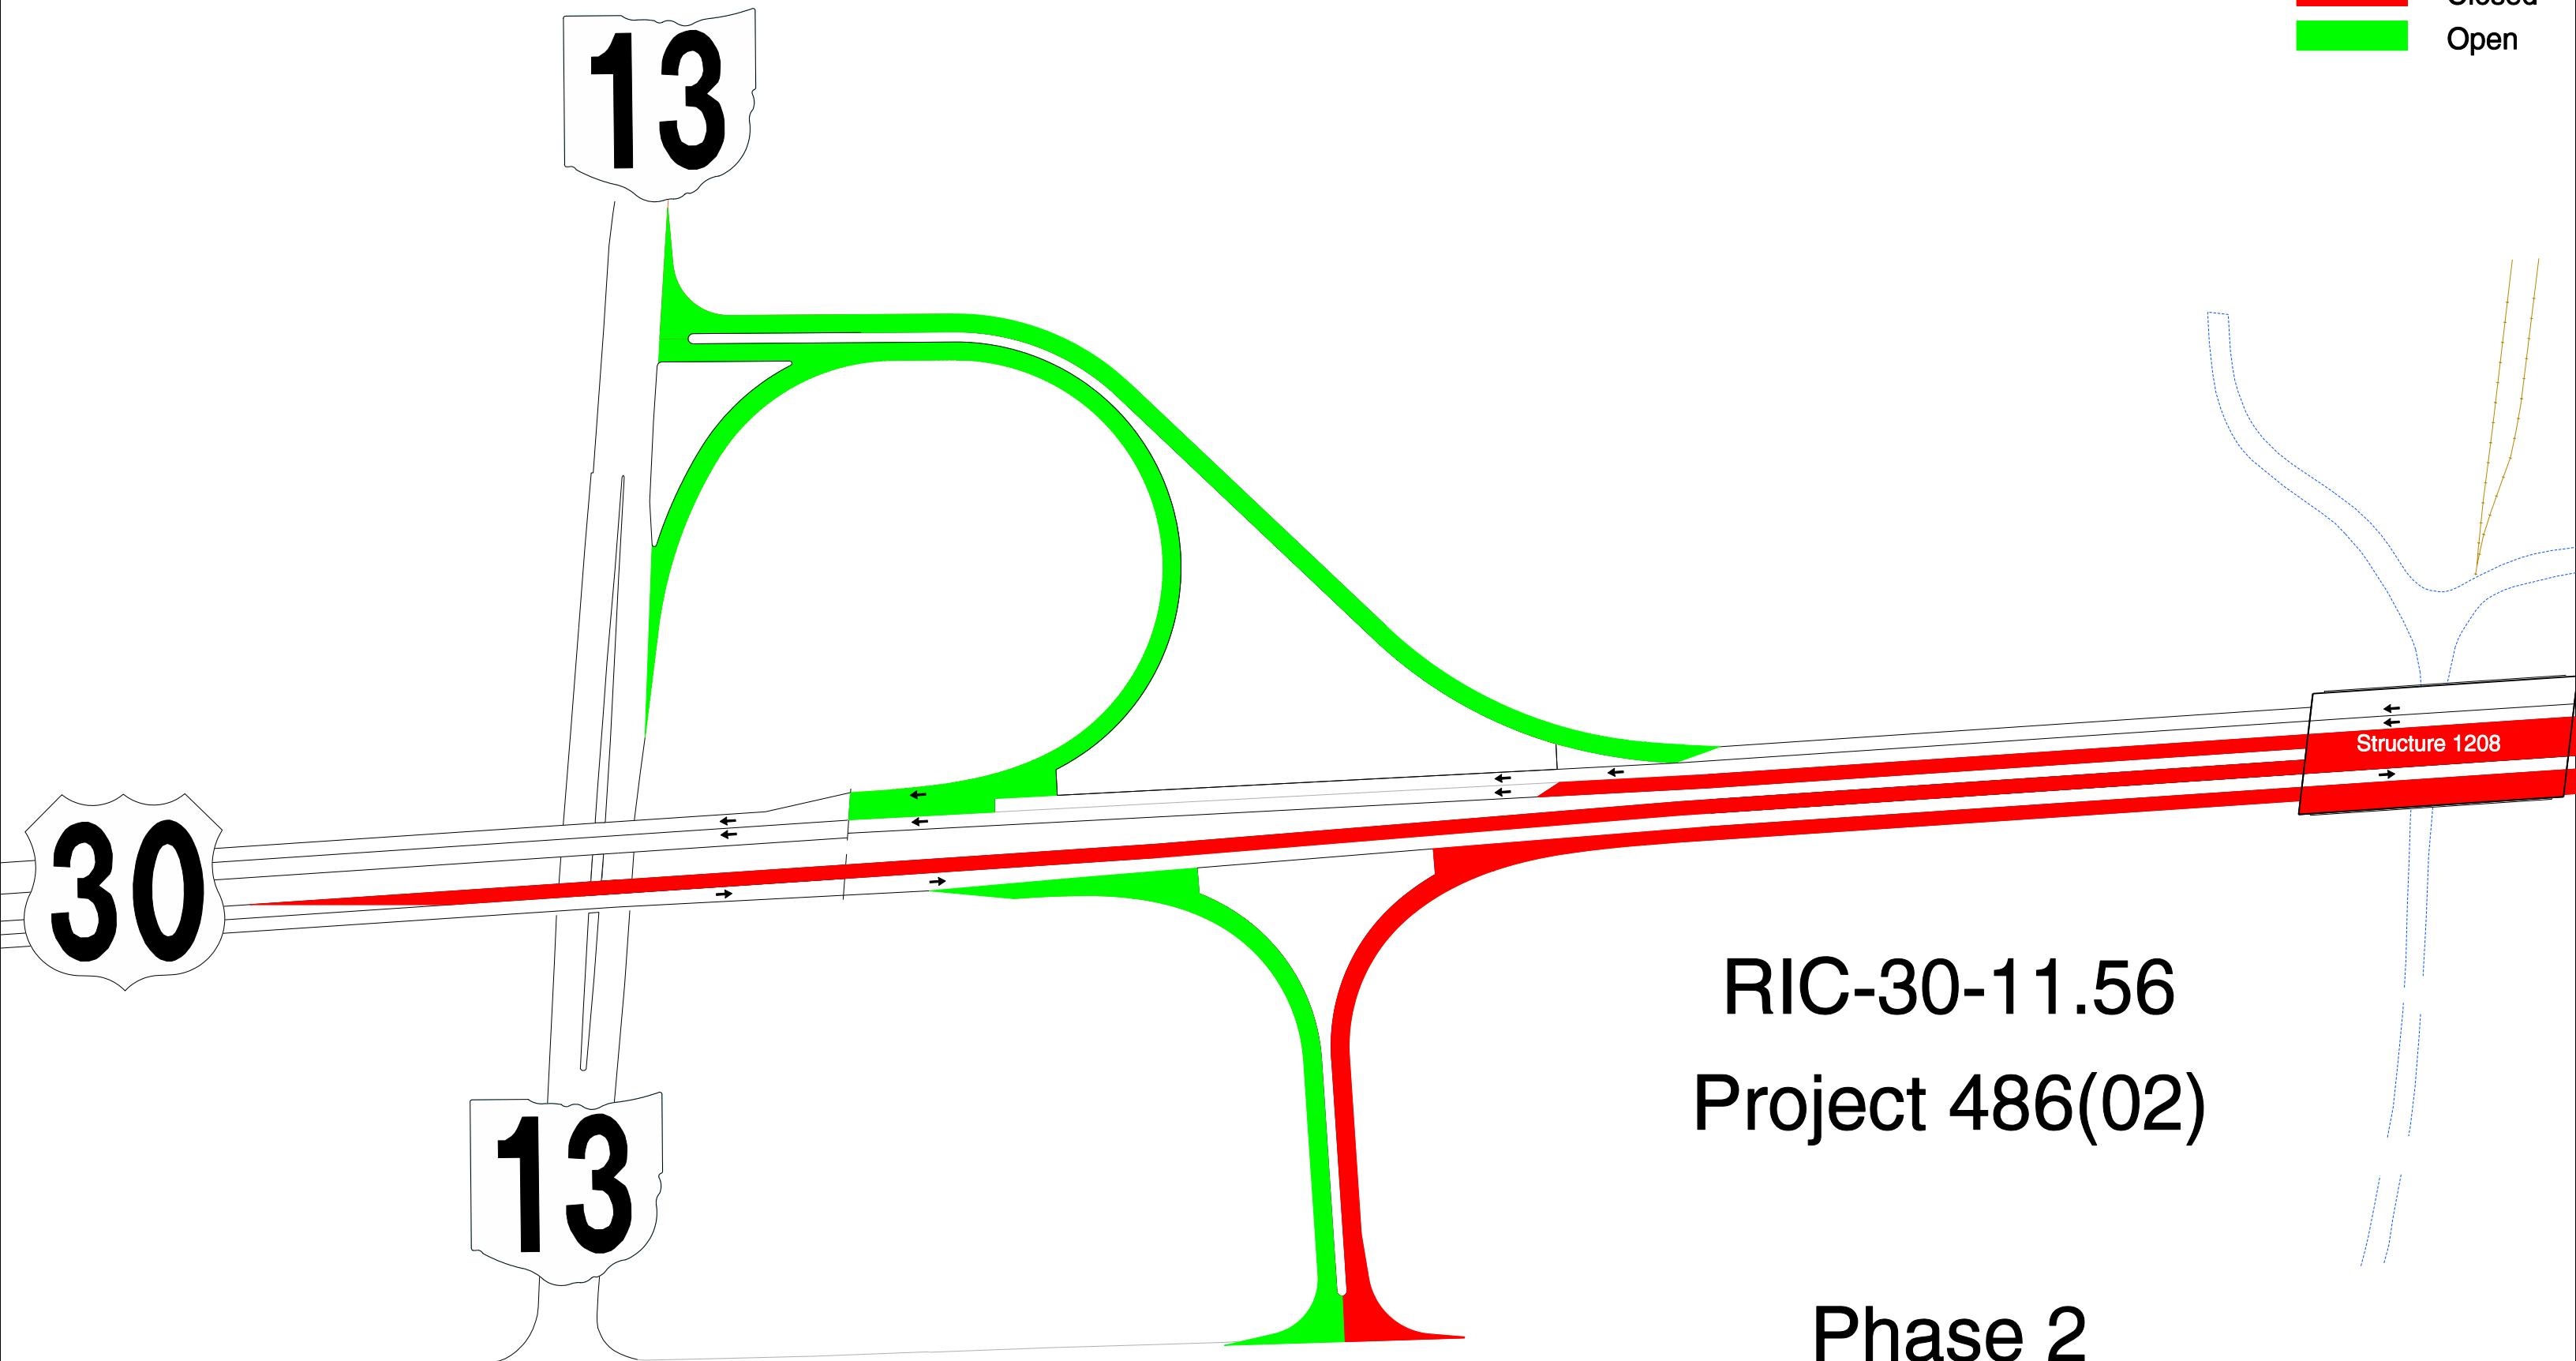

RIC-30-11.56  
Project 486(02)

Phase 2

July 1, 2003 to October 31, 2003

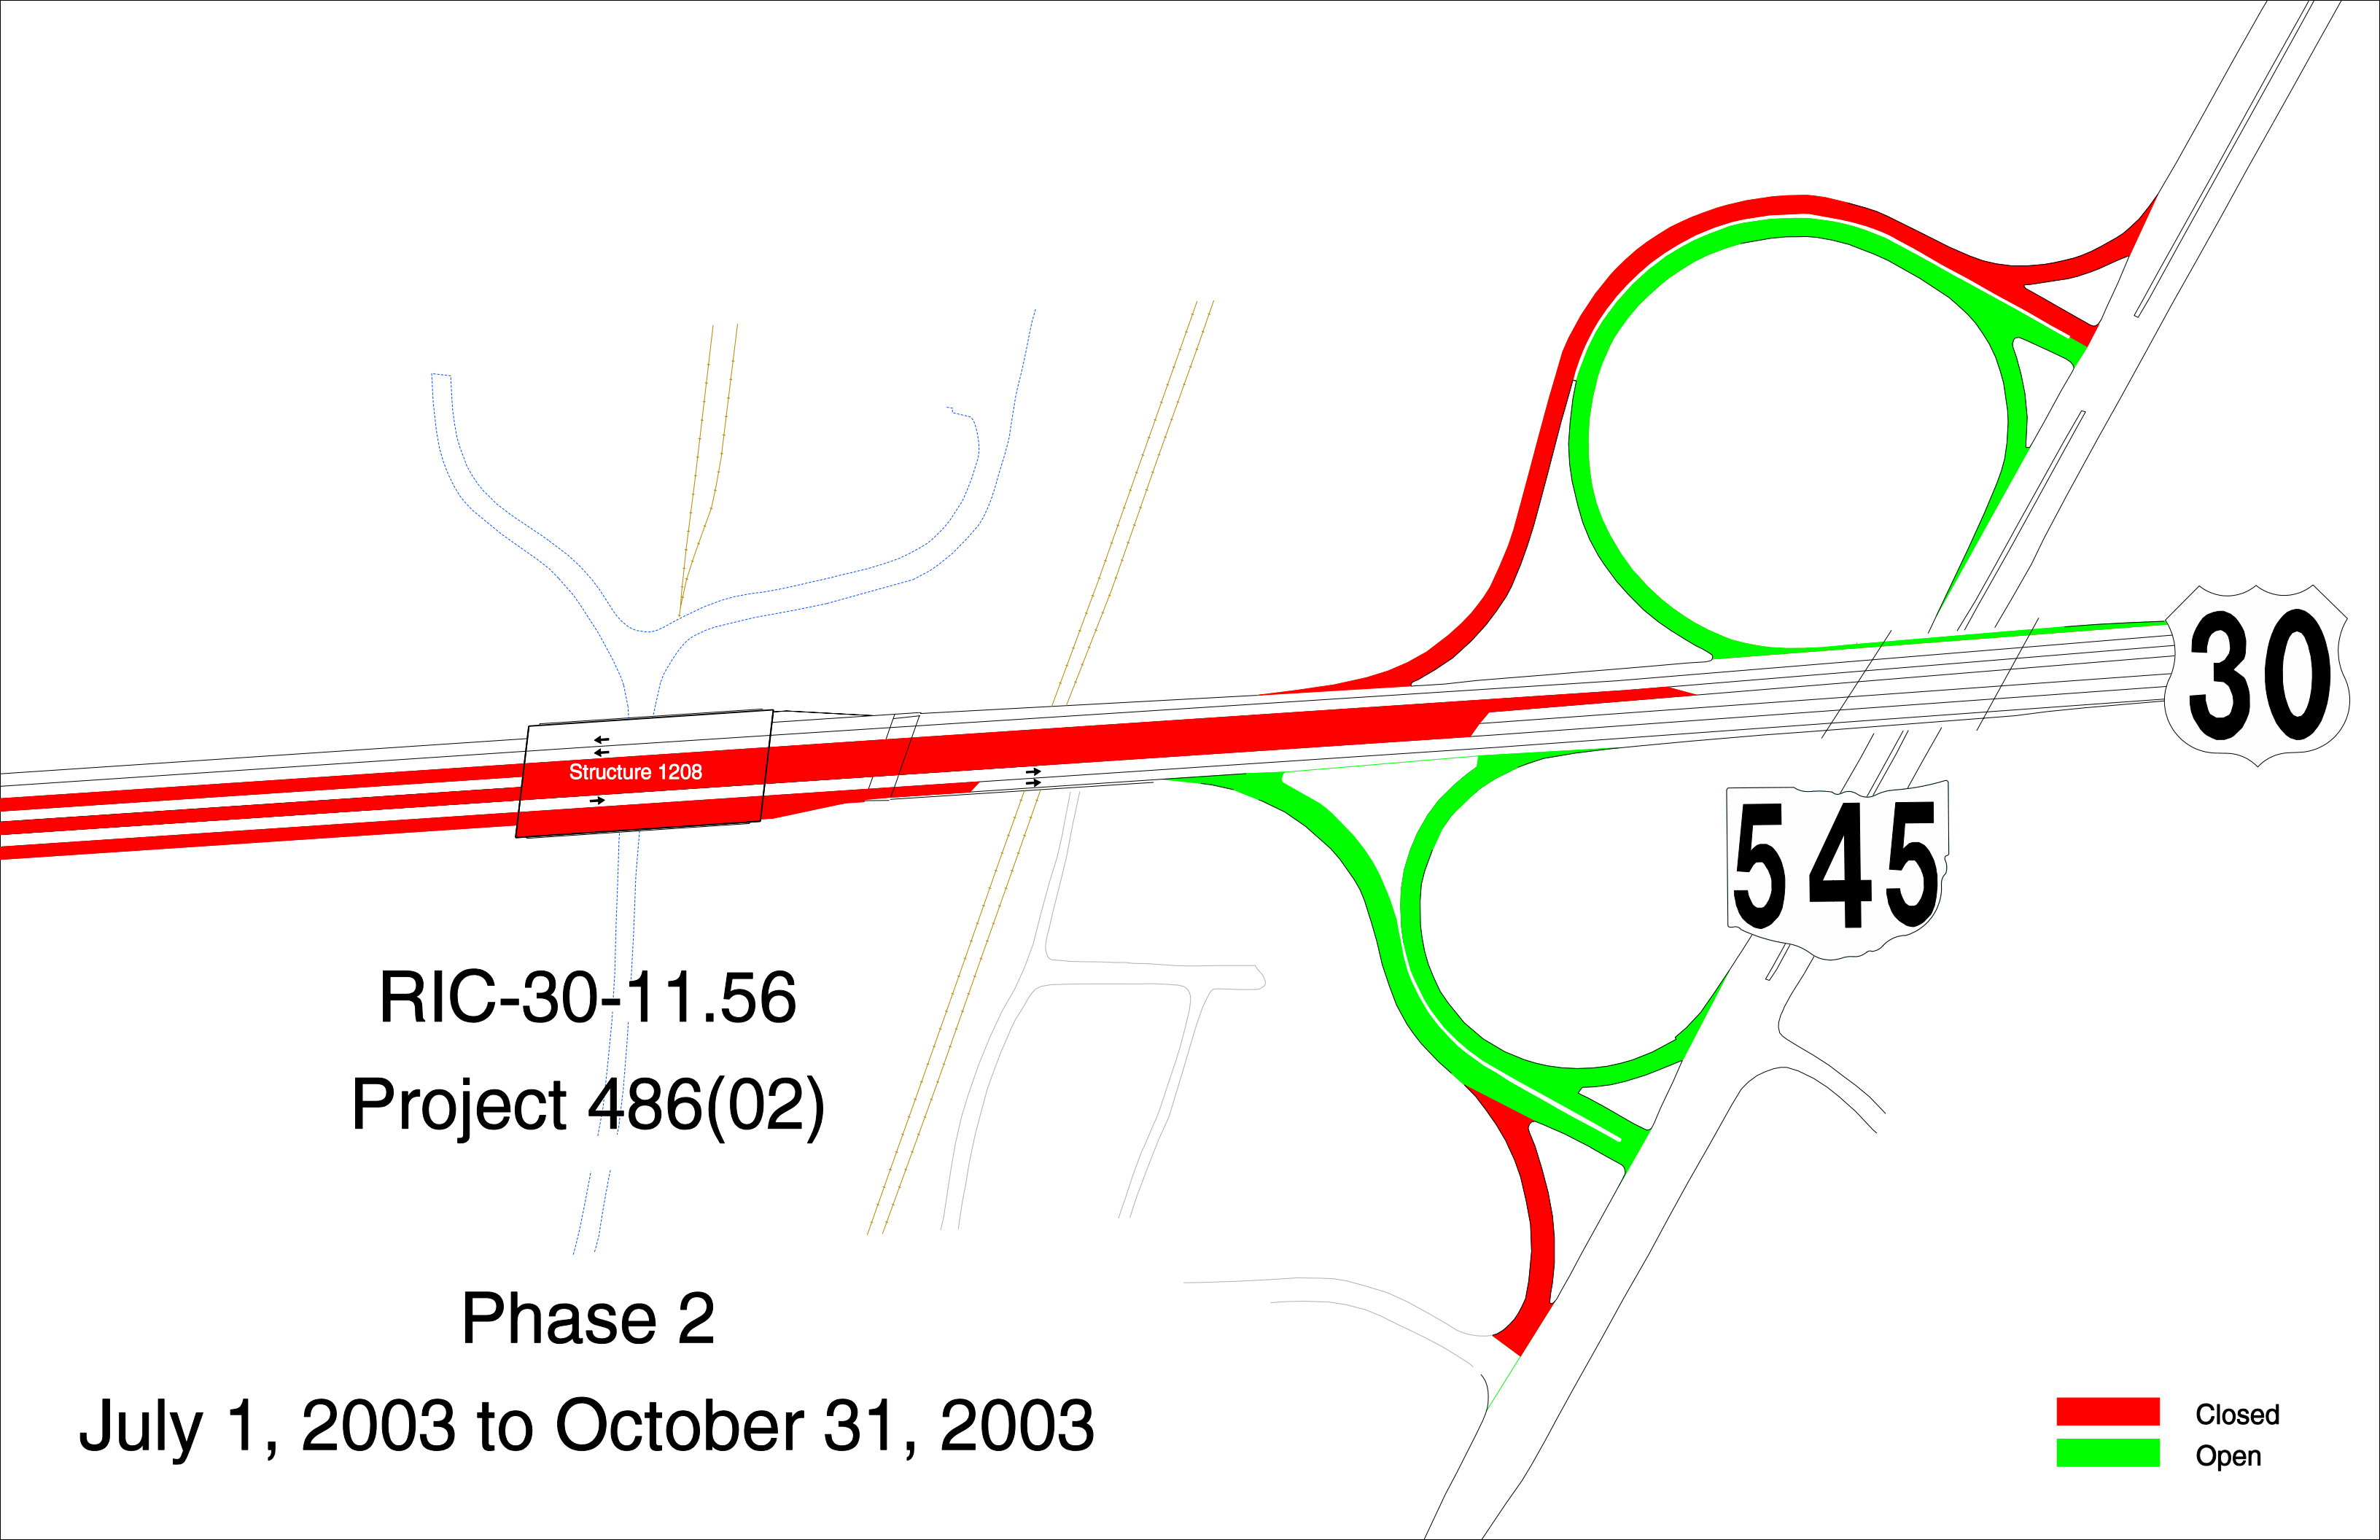

Structure 1208

30

545

RIC-30-11.56  
Project 486(02)

Phase 2

July 1, 2003 to October 31, 2003

Closed  
Open

**RIC-30-11.56  
Project 486(02)**

**Between Phase 2 & Phase 3  
(November 20, 2003 to February 29, 2004)**


- ✓ Two Lanes of Traffic each direction.
- ✓ All SR-13 and SR-545 ramps open.
- ✓ No work on roadway or pavement during this winter period.
- ✓ Complete pier and abutment outside phase structure 1157 L&R
- ✓ Maintain temporary signal at SR-545/Longview in “Flash” operation.

**RIC-30-11.56**  
**Project 486(02)**

**Phase 3**  
**(March 1, 2004 to May 31, 2004)**

- ✓ Finish outside phase of Structure 1157 bridge deck
- ✓ Two lanes each direction (except for a four week period)
- ✓ Close and reconstruct all SR-13 ramps. US 30 Eastbound entrance ramp from SR-13 open by May 14. US 30 Westbound exit ramp to SR-13 open by May 28. (Weather permitting.)
- ✓ Maintain temporary signal at SR-545/Longview
- ✓ All SR-545 ramps open.

# RIC-30-11.56 Project 486(02)

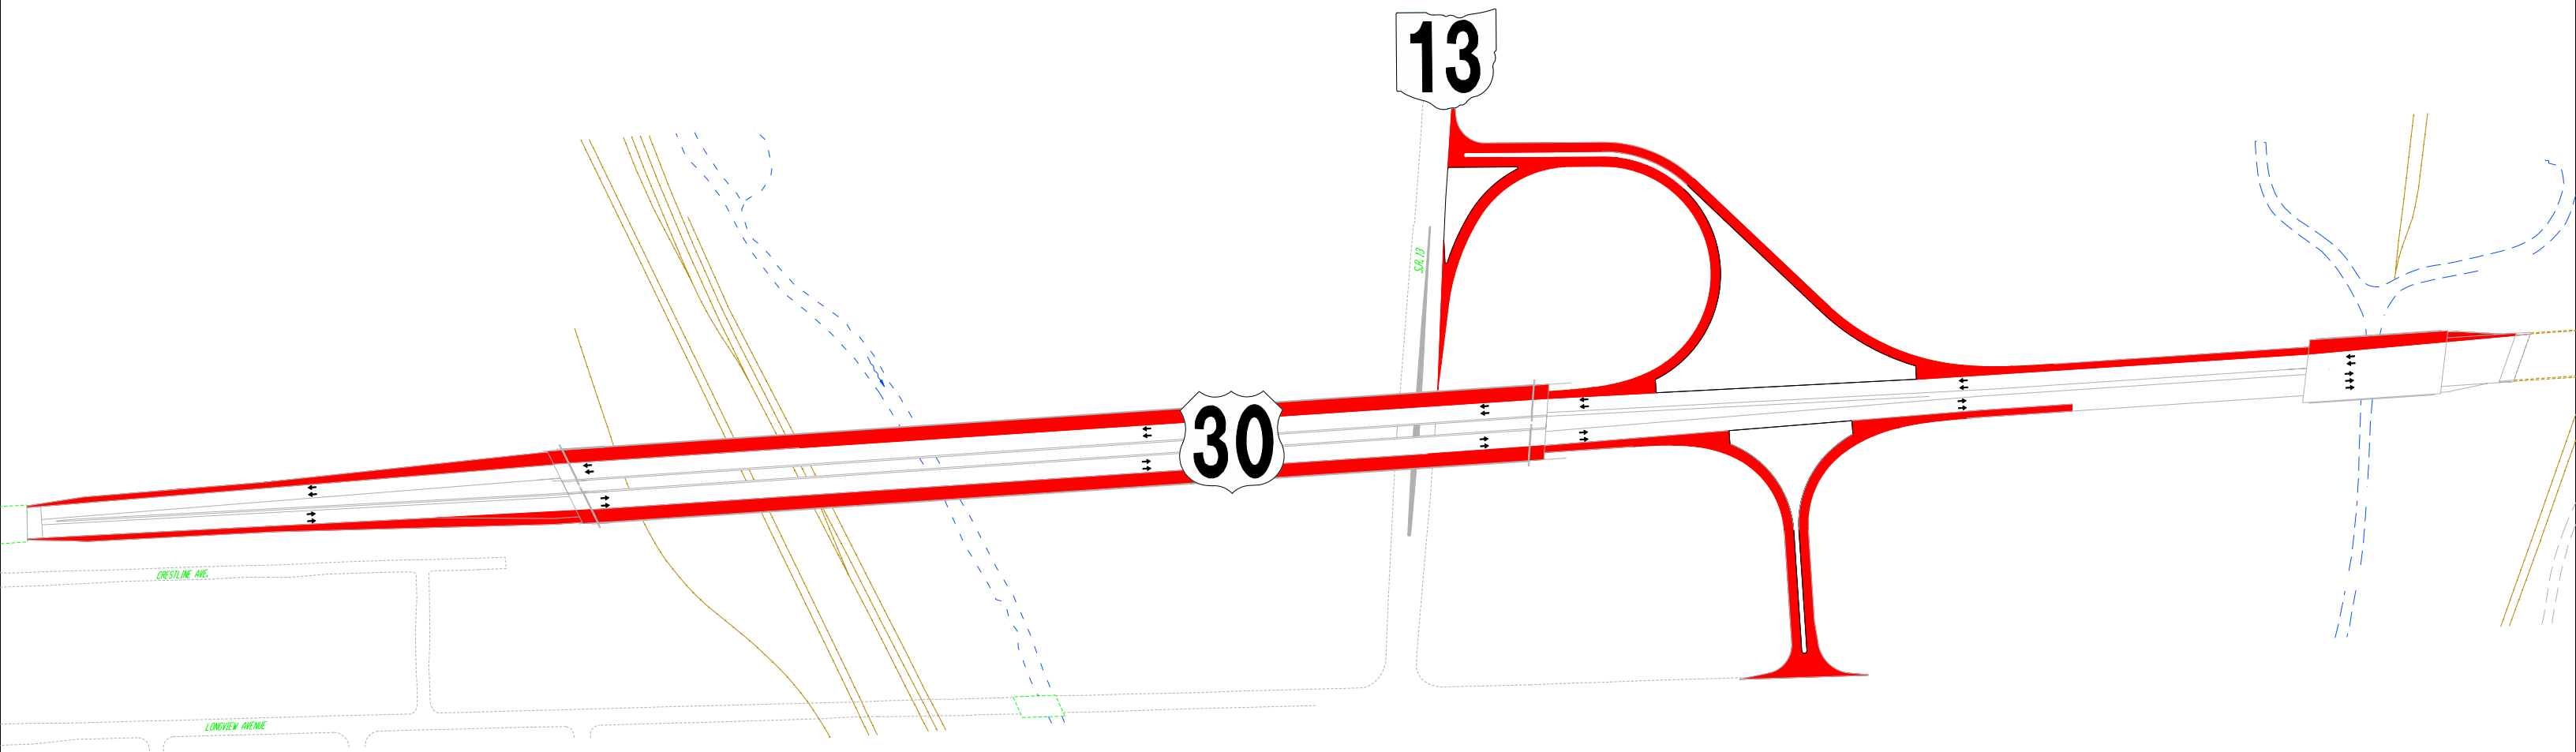

## Phase 3

March 1, 2004 to May 31, 2004


■ Closed  
■ Open

**RIC-30-11.56  
Project 486(02)**

**Phase 4  
(June 1, 2004 to August 30, 2004)**

- ✓ Begin inside phase of Structure 1157
- ✓ Two lanes of traffic each direction on new bridge.
- ✓ US 30 Westbound entrance ramp from SR-13 and eastbound exit ramp to SR-13 remain closed.
- ✓ US 30 Eastbound entrance ramp from SR-13 and westbound exit ramp to SR-13 shall be open.
- ✓ Temporary traffic signal still operating at SR-545/Longview
- ✓ All SR-545 ramps open.

# RIC-30-11.56 Project 486(02)

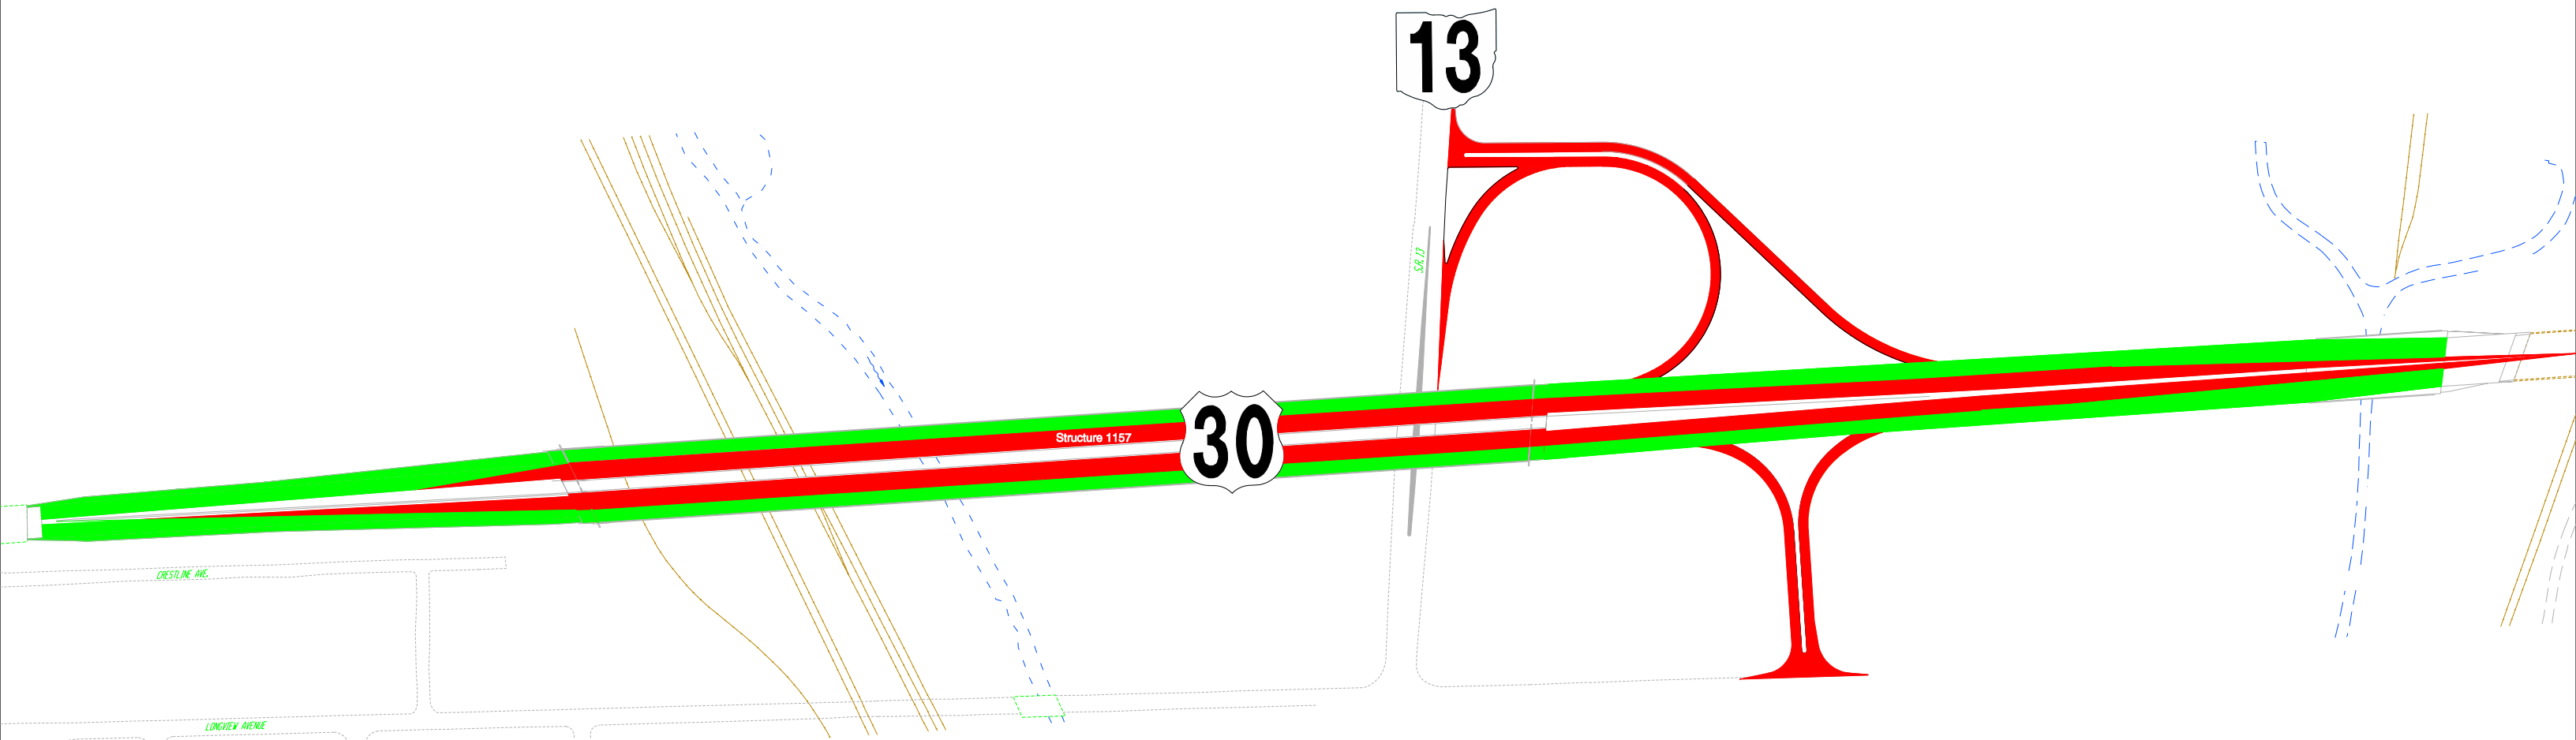

Phase 4

June 1, 2004 to August 30, 2004


 Closed  
 Open

**RIC-30-11.56  
Project 486(02)**

**Phase 4a & 4b  
(September 1, 2004 to June 30, 2005)**

- ✓ Finish ramps and inside phase of Structure 1157
- ✓ Two lanes of traffic each direction.
- ✓ Westbound entrance Ramp from SR-13 and eastbound exit ramp to SR-13 shall remain closed.
- ✓ Eastbound entrance ramp from SR-13 and westbound exit ramp to SR-13 shall be open.
- ✓ Temporary traffic signal still operating at SR-545/Longview

# RIC-30-11.56 Project 486(02)

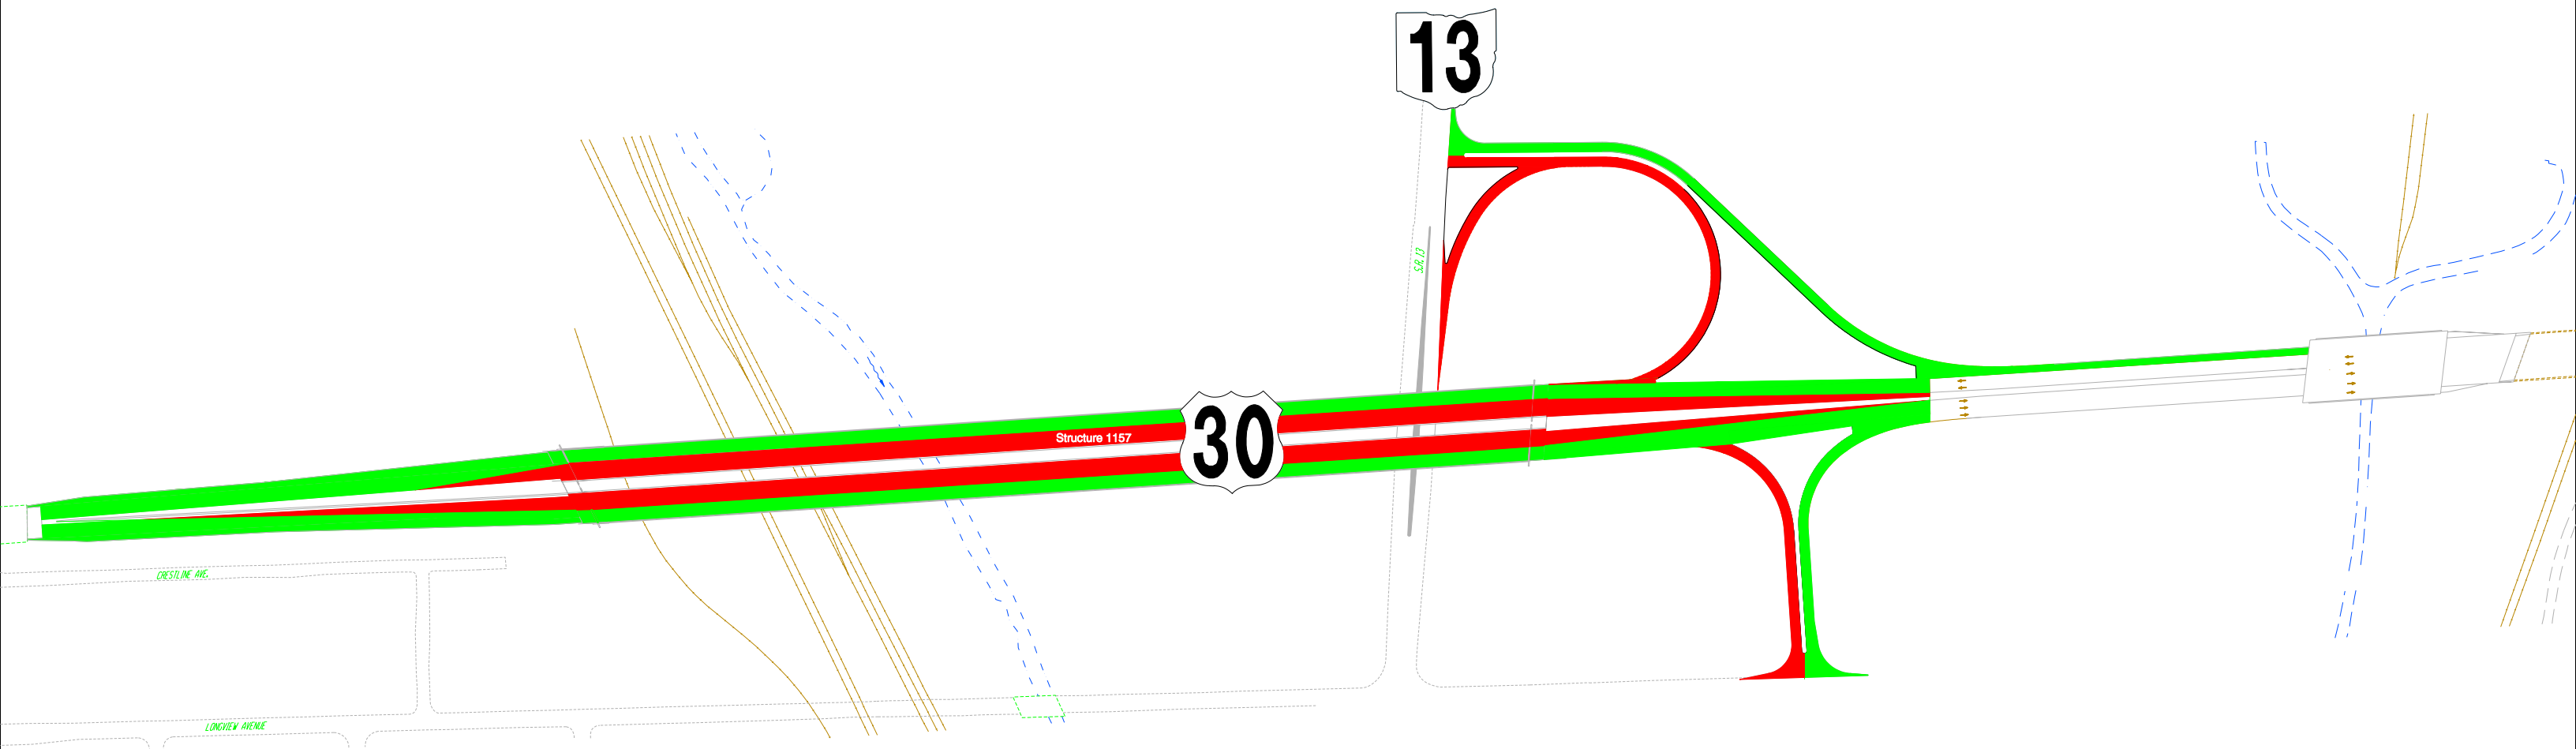

## Phase 4a & 4b

September 1, 2004 to June 30, 2005

 Closed  
 Open


**RIC-30-11.56**  
**Project 486(02)**

**Phase 5**  
**(July 1, 2005 to July 31, 2005)**

- ✓ Maintain two lanes of traffic each direction, except during working hours where one lane in each direction will be allowed to place the final surface course on US-30 mainline & SR-13 ramps.
- ✓ All ramps open.

# RIC-30-11.56


## Project 486(02)

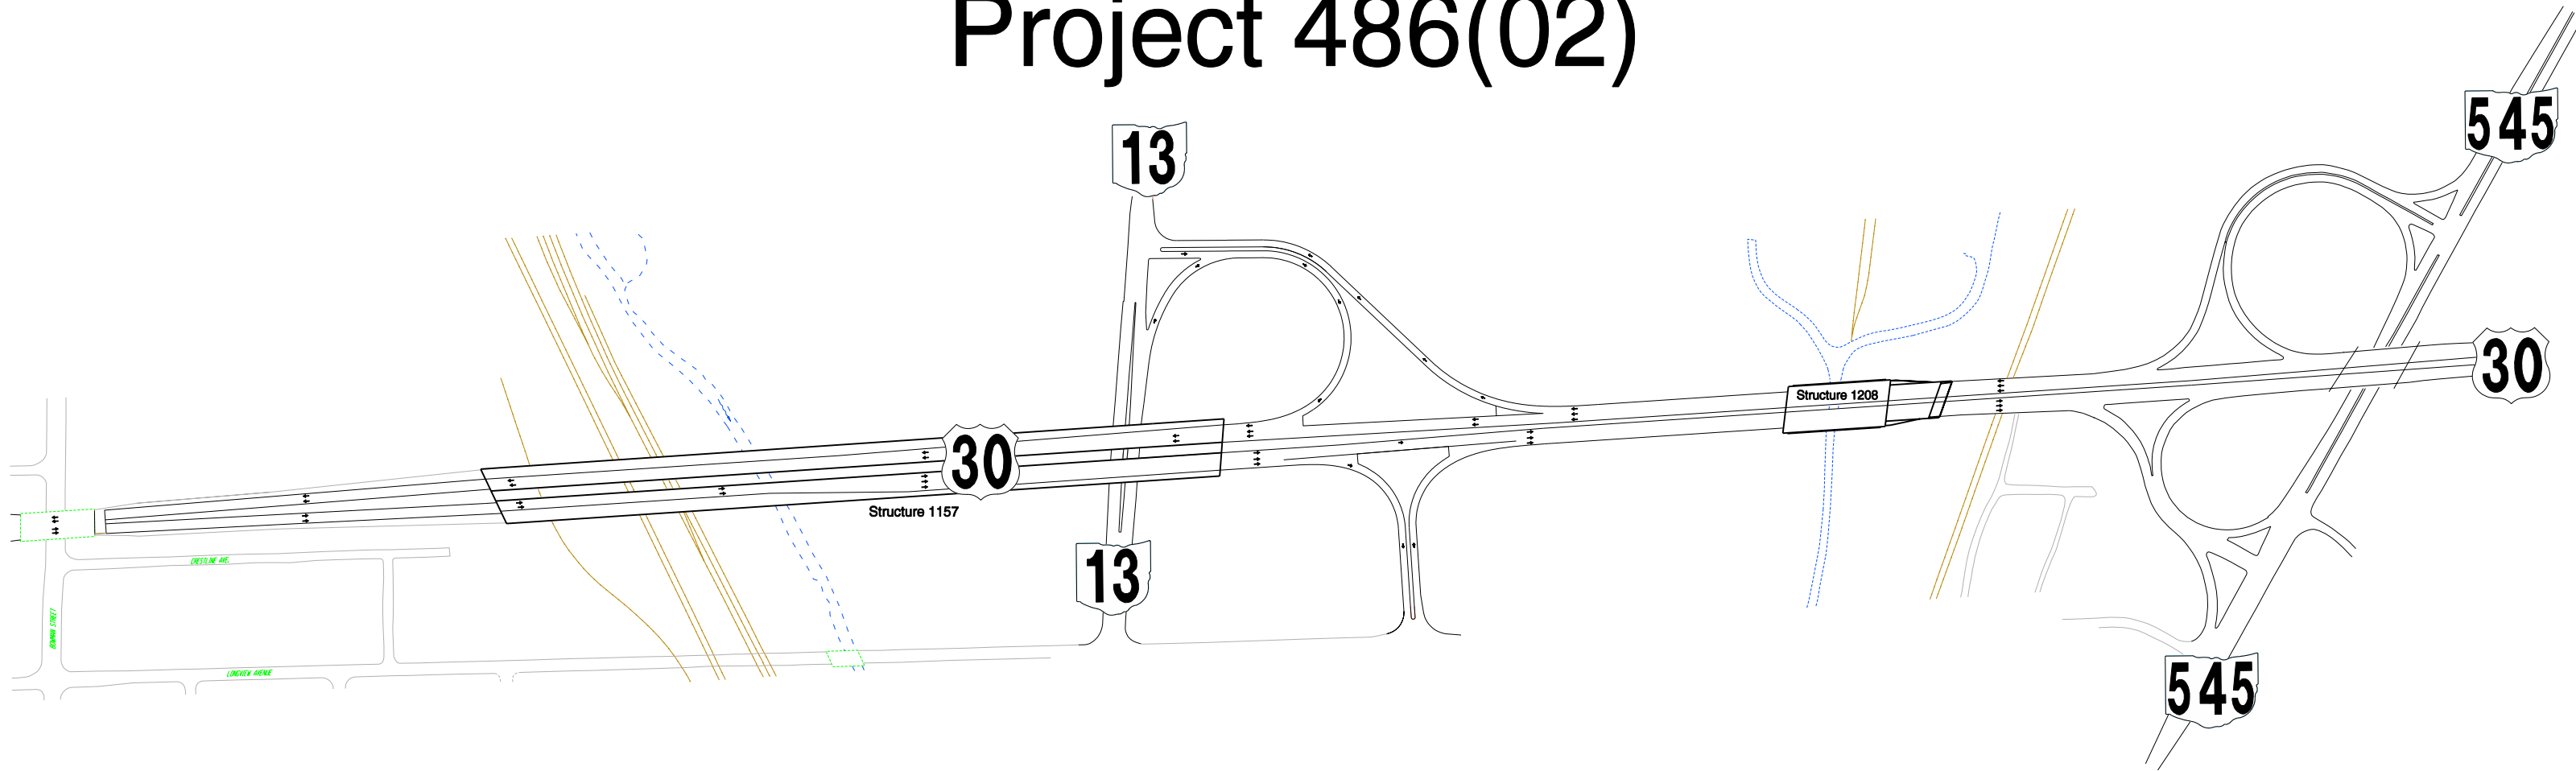

### Finished Project

# RIC-30-11.56


## Project 486(02)

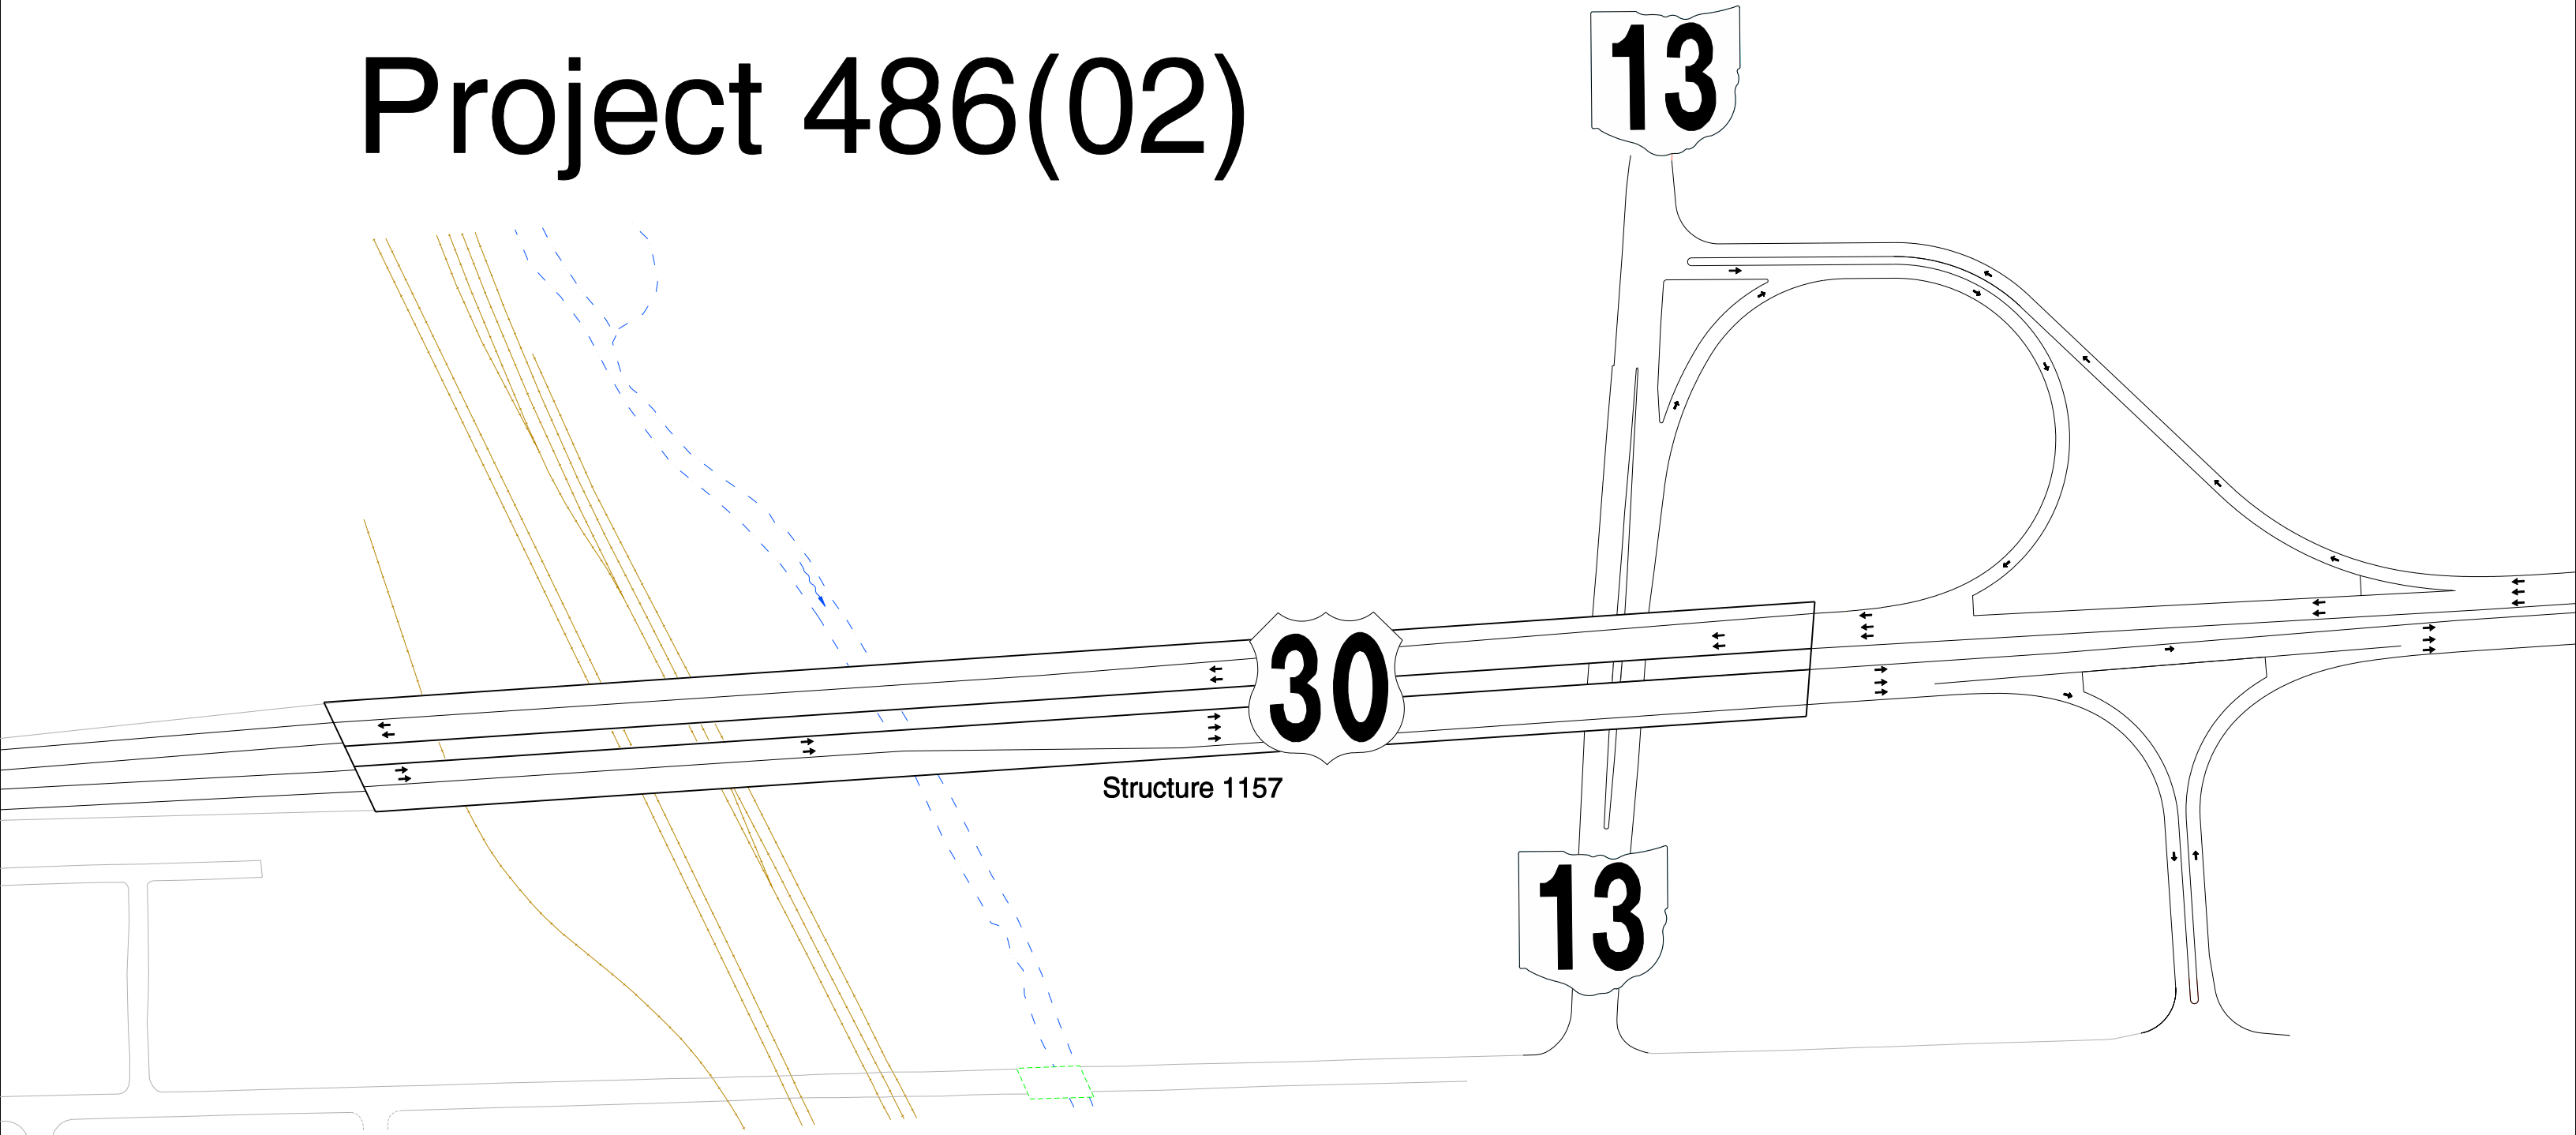

# Finished Project

# RIC-30-11.56

## Project 486(02)

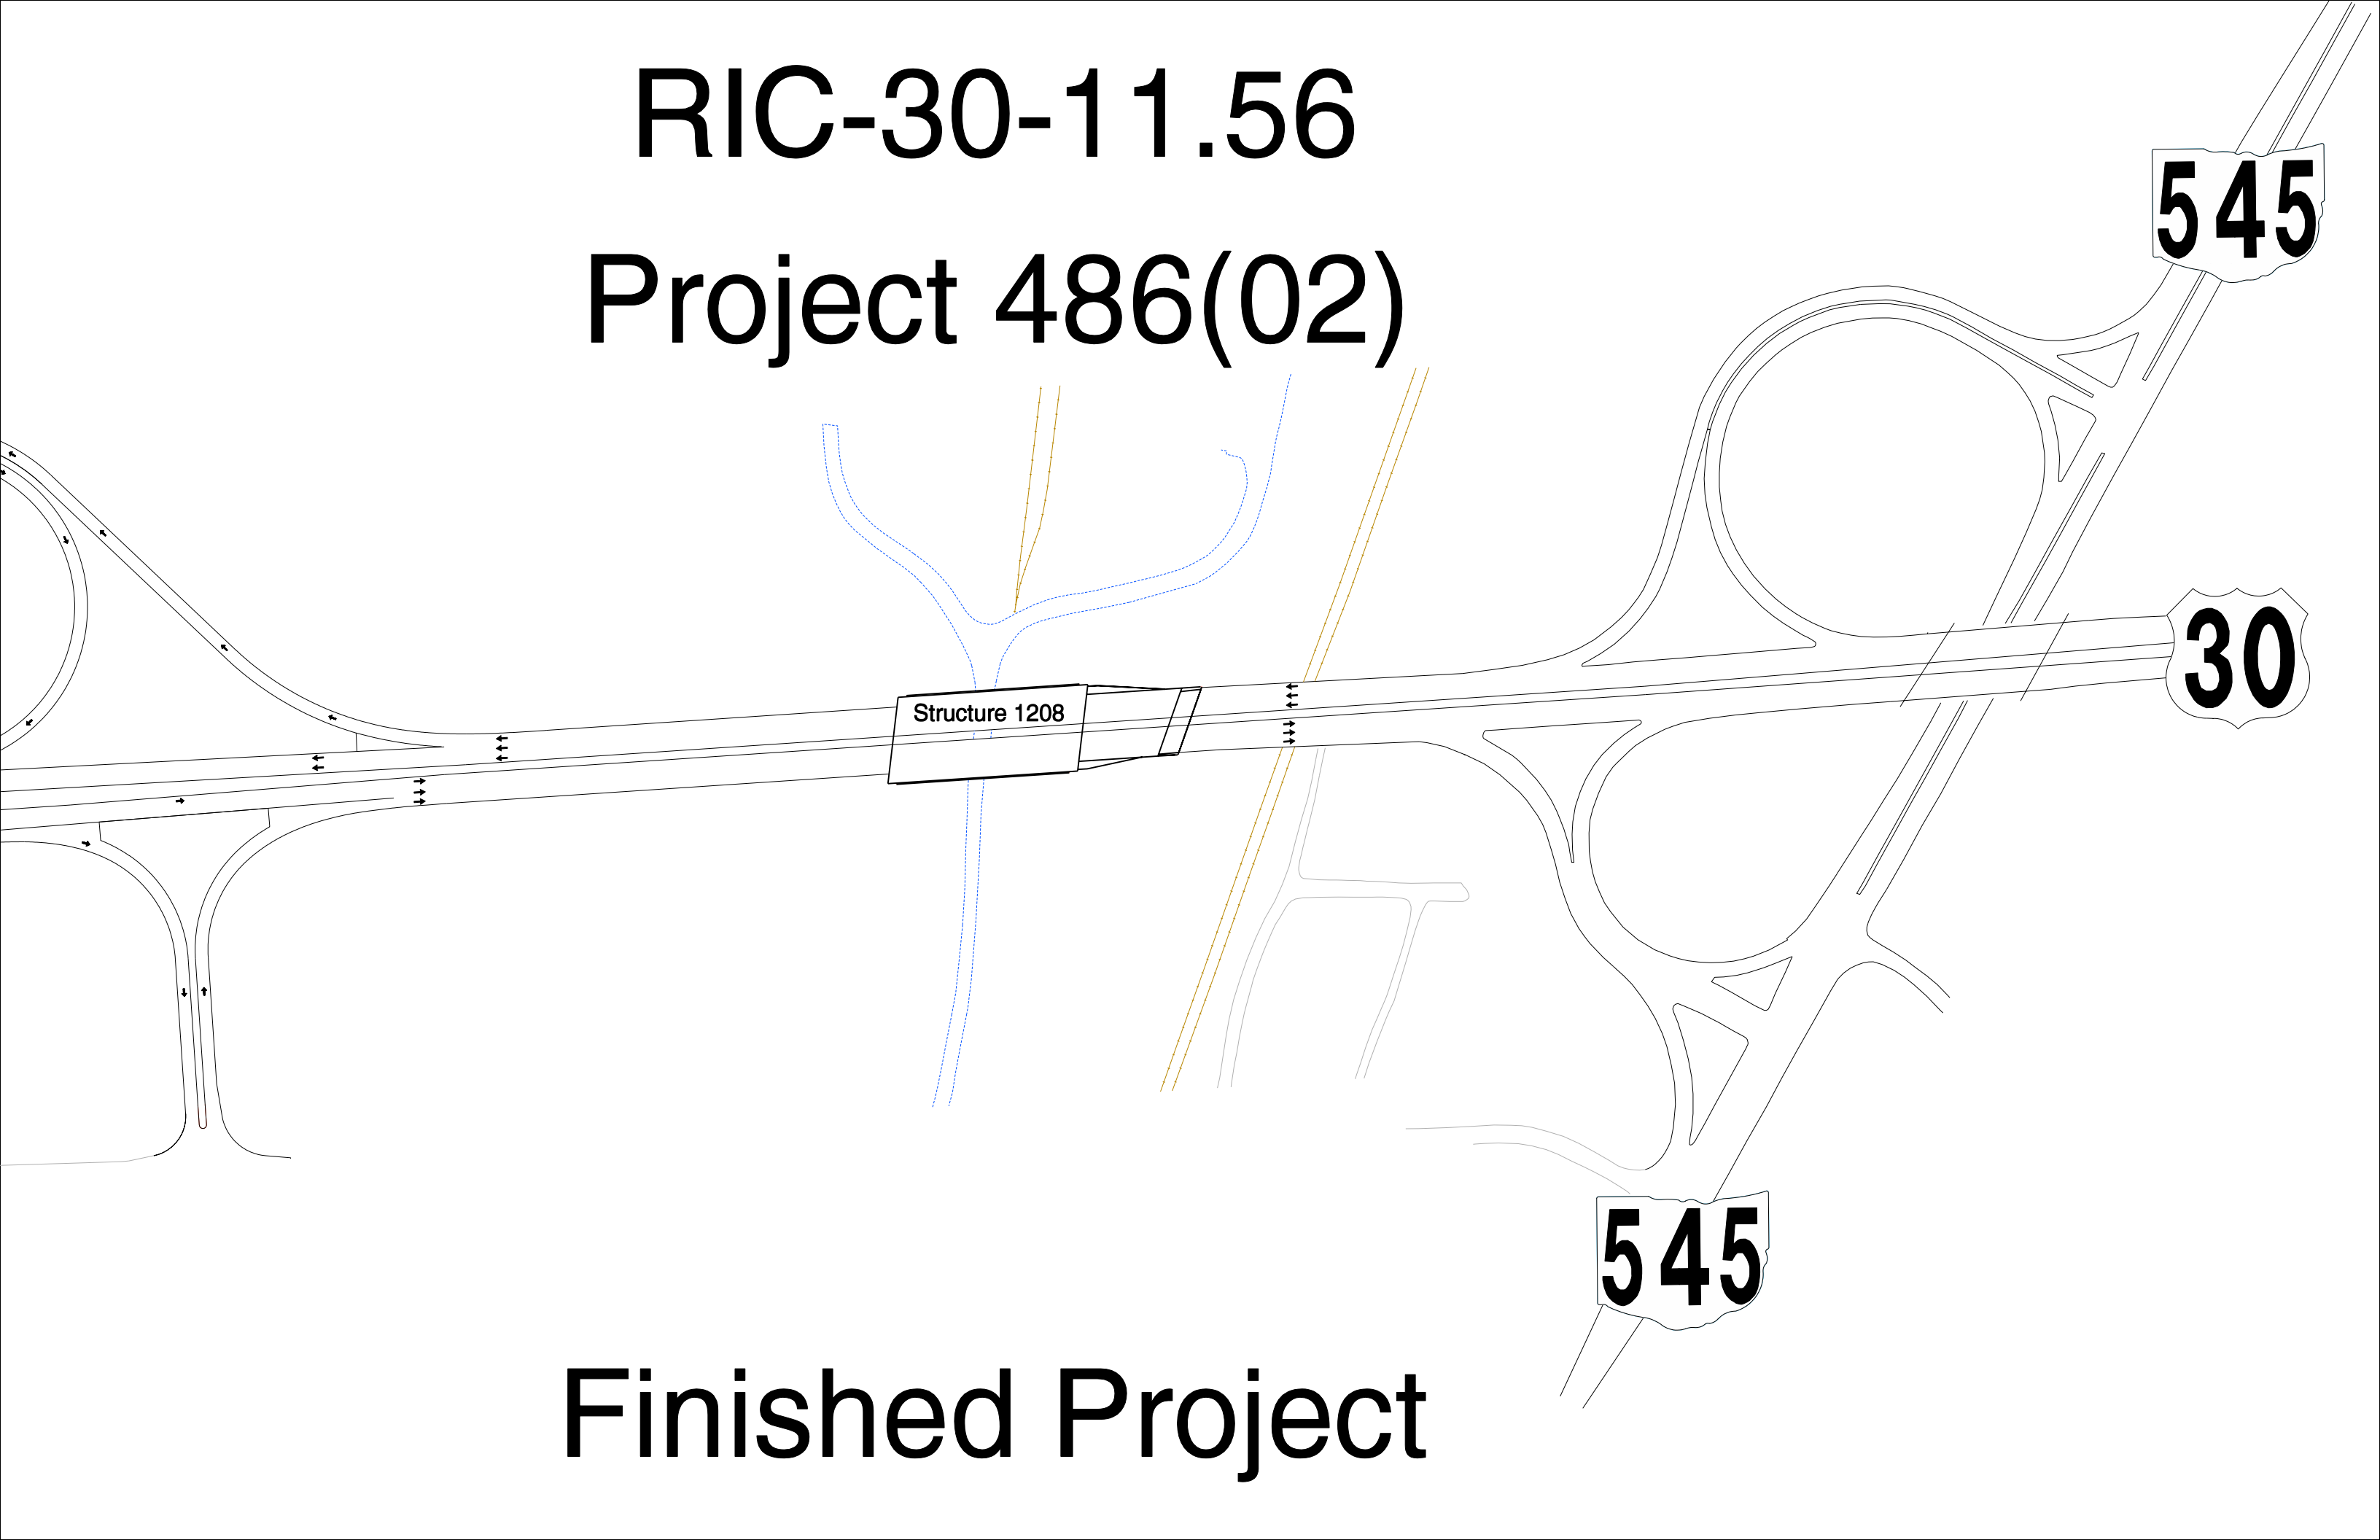

# Finished Project
